

Ames

OK

AD-616 908

ULTRASONIC WELDING PROCESS AND EQUIPMENT FOR CONSTRUCTION OF ELECTRON-TUBE MOUNTS

B061227

Eleventh Quarterly Progress Report
For the Period
January 1 through March 31, 1965

Contract No. DA-36-039-sc86741
Order No. 19063-PP-62-81-81

Placed by
Industrial Engineering Division
United States Army Electronics Command
225 South Eighteenth Street
Philadelphia, Pennsylvania

AEROPROJECTS INCORPORATED
West Chester, Pennsylvania

ULTRASONIC WELDING PROCESS AND EQUIPMENT
FOR CONSTRUCTION OF ELECTRON-TUBE MOUNTS

Eleventh Quarterly Progress Report
For the Period
January 1 through March 31, 1965

The object of this program is to design and construct prototype welding equipments and their associated accessories to perform by ultrasonic techniques the welding operations required in the assembly of electron tubes.

Contract No. DA-36-039-sc86741
Order No. 19063-PP-62-81-81

Specifications SCS-114A, SCIPPR-15
and MIL-E-1/1121A

Report Prepared by:

J. S. Thomas

Report Approved by:

J. Byron Jones

ABSTRACT

Fabrication of redesigned tooling for use with the 600-watt welder was completed. Satisfactory performance was established during the fabrication of 36 sub-assemblies, and a complete 6080WB electron-tube mount was obtained using the new tooling and a modified assembly sequence. The welder with tooling was then redelivered to Tung-Sol, and operator training was initiated. Also, a precision fixture for crimping stem leads was designed and fabricated.

Extraction from W-Repair and Assembly
Components welding has been delayed by the effort required for the redesign of tooling. However, design studies of a 600-watt welder with special low clamping forces for welding frame grids have been initiated.

TABLE OF CONTENTS

	<u>Page</u>
ABSTRACT	ii
PURPOSES	1

NARRATIVE AND DATA

I	ELECTRON TUBE STUDY	2
	A. Tung-Sol Activity	2
	B. Aeroprojects Activity	2
II	COMPONENTS WELDING	5
	A. Tungsten-Rhenium Wire Welding	5
	B. Frame-Grid Welding	5
III	CONCLUSIONS	10
	PROGRAM FOR NEXT INTERVAL	10
	PUBLICATIONS AND REPORTS	11
	TECHNICAL MAN-HOURS EXPENDED DURING THIS REPORT PERIOD	12
	PROJECT SCHEDULE	14

LIST OF FIGURES

<u>Figure</u>		<u>Page</u>
1	Redesigned Welding Tips T-4 and T-5	3
2	Fixture for Precision-Crimping of Stem Leads	4
3	6080WB Electron-Tube Mount Welded with the Revised Tooling.	6
4	Modified Anvil Fixture A-5	7

LIST OF TABLES

<u>Table</u>		<u>Page</u>
I	Assembly Sequence for 6080WB Tube	8

PURPOSES

The objectives of this Production Engineering Measure (PEM) are to:

1. Demonstrate the capability limits of ultrasonic welding to join combinations of metallic materials of interest to the electron-tube industry. Devote major effort to making satisfactory joints in materials and geometries which might be difficult or impossible to join by other means.
2. Analyze the welding requirements for a specific electron tube - Type 6080WB. This type was selected by the U. S. Army Electronics Command because it has a record of rejects and failures due to metallic splatter caused by conventional welding techniques and improperly welded joints.
3. Redesign components of the Type 6080WB electron-tube where possible, to permit ultrasonic welding of joints previously found impractical. This effort will result in a tube mount with as many metal-to-metal joints as possible produced by ultrasonic welding so that evaluation of electron-tube performance will not be confused by the influence of metal-to-metal joints produced by other welding or joining techniques.
4. Determine the feasibility of joining 0.003-inch gold-plated molybdenum grid wires to 0.060-inch molybdenum side bars by ultrasonic welding for frame grid manufacture. If successful, redesign applicable components of the Type 6080WB electron-tube mount to permit the use of frame grids.
5. Prepare fixturing and tooling for the Type 6080WB electron tube, compatible with ultrasonic welding equipment.
6. Ultrasonically weld the parts required to assemble electron-tube mounts for the 6080WB tube type, and compare results obtained against similar sub-assemblies made by conventional joining methods. Tests will include strength and environmental tests.
7. Build production ultrasonic welding equipment which will enable an electron-tube manufacturer to make the welded connections in a broad range of electron-tube types.
8. Install the ultrasonic welding equipment in a production company, and produce on a pilot basis with that company's personnel a limited lot size of Type 6080WB electron tubes for subsequent evaluation in accordance with the applicable military specification.

NARRATIVE AND DATAI. ELECTRON TUBE STUDYA. Tung-Sol Activity

The 600-watt ultrasonic welder and the redesigned and fabricated tools were delivered to Tung-Sol near the end of this period on March 17, 1965. A training program was initiated for the new operator assigned to the task of electron-tube fabrication. On March 18 Messrs. T. A. Walraven and J. G. Thomas of Aeroprojects explained the tooling changes and demonstrated the assembly sequence through step 6C (see Table I) to the Tung-Sol operator and Mr. Norman Helmstetter. Mr. Max Yarmovsky of Tung-Sol also attended the welding demonstrations.

Since a single operator will carry out the entire assembly sequence, the training for each step will precede the fabrication of each sub-assembly in order to effect a saving in time. Upon partial completion of the sample lot of 6080WB electron tubes through step 6C, the remaining steps of the assembly sequence will be reviewed and demonstrated by Aeroprojects personnel at Tung-Sol in preparation for fabrication of the entire sample lot of completely assembled electron tubes.

B. Aeroprojects Activity

During the last period (Quarterly Progress Report No. 10) the tooling designed for use with the 600-watt ultrasonic welder in assembly of the 6080WB electron tube exhibited service weaknesses when put into production. Tooling redesign and fabrication of revised tooling were completed during this period. Welding tips T-4 and T-5 were evaluated for welding performance, and satisfactory welds were achieved. These redesigned tips are shown in Figure 1.

A fixture for precision crimping the stem leads was also designed, fabricated, and tested. The tool previously used for this operation was a pair of pliers with contoured jaws to provide the crimp. Although this tool offered a satisfactory method, care was required to locate the position and angular orientation of the crimp on each of the eight stem leads (Quarterly Progress Report No. 6, Fig. 8). The new precision crimping fixture, shown in Figure 2, incorporates the punch and die in a spring-loaded precision die set. The glass stem is accurately positioned in a housing mounted on a wayslide. Each stem lead is indexed into position for crimping in two steps: (1) rotation to a stop provided by a detent mechanism within the stem housing and (2) adjustment of the stem lead between the punch and die faces. This fixture thus provides stem leads which contain uniform crimps accurately located in reference to the stem base.

Card 2/4

61227

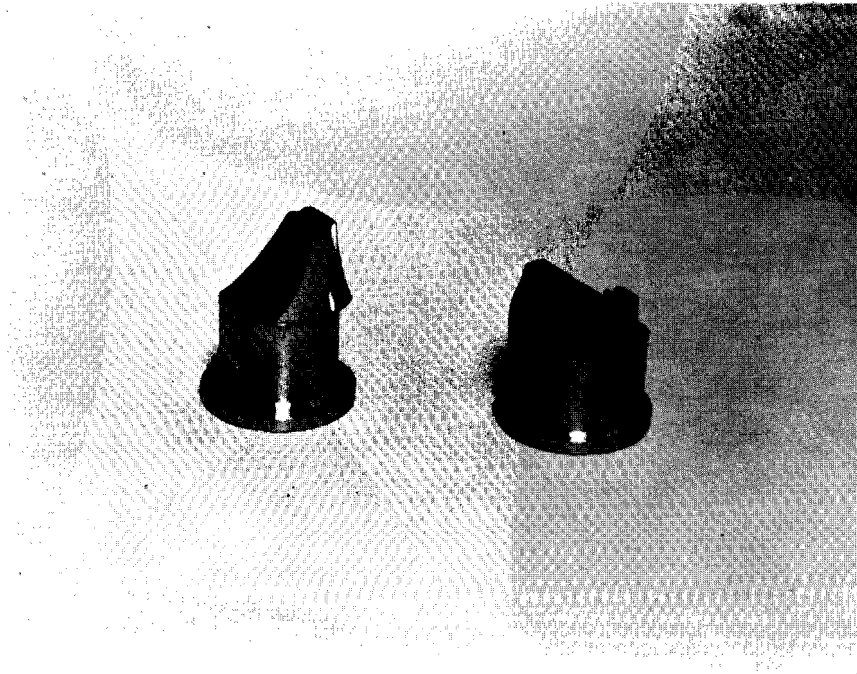


Figure 1

REDESIGNED WELDING TIPS T-4 AND T-5
(Scale 1:1)

W, Mo, A

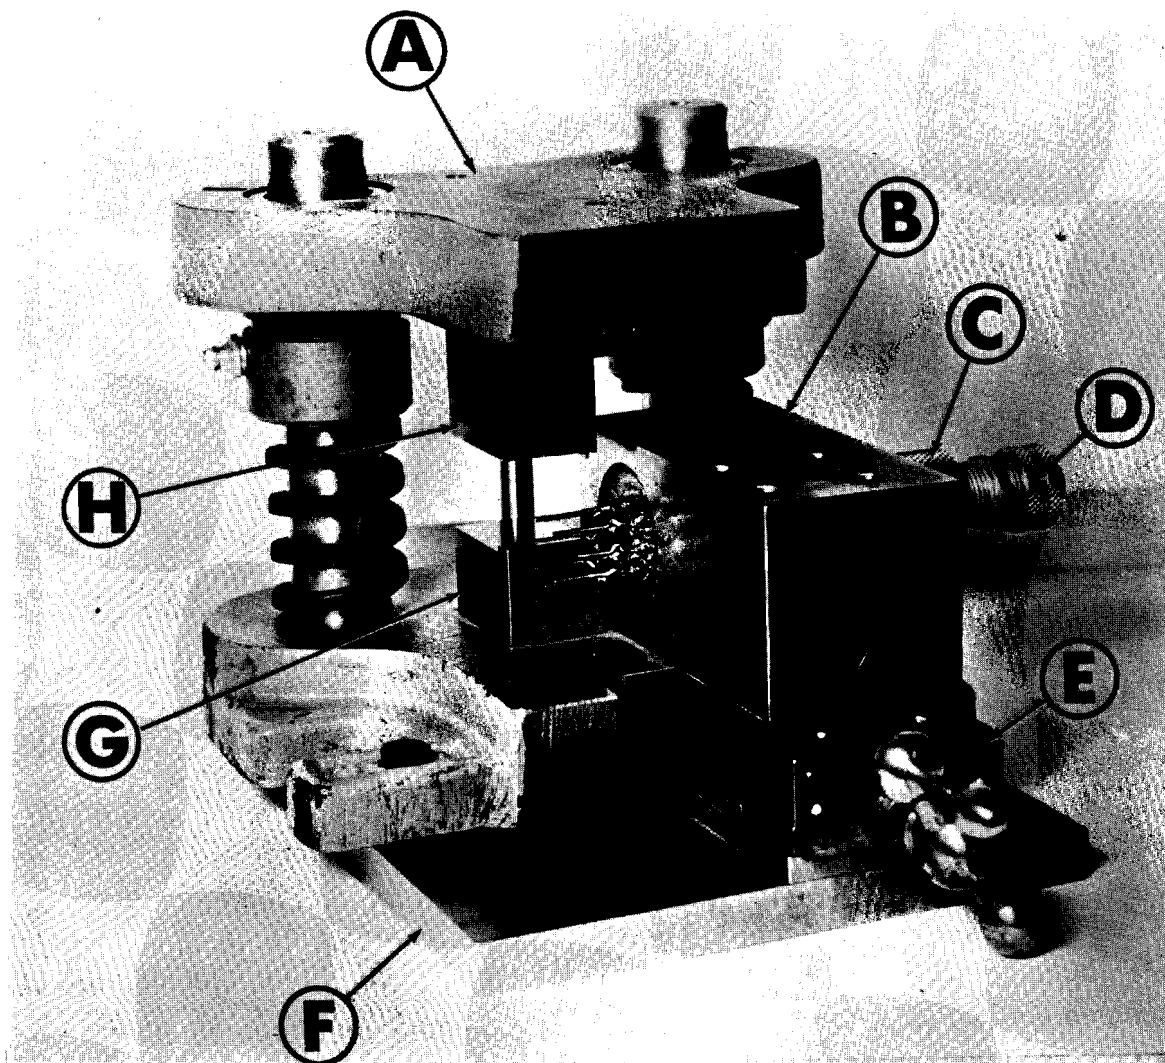


Figure 2

FIXTURE FOR PRECISION-CRIMPING OF STEM LEADS

- | | |
|--|-------------------------------------|
| A - Die Set | D - Stem Clamp |
| B - Bearing Block (with detent in rear for stem holder indexing) | E - Way Slide (advance and retract) |
| C - Stem Holder (with index slot for stem) | F - Base Plate |
| | G - Lower Die |
| | H - Upper Die |

During evaluation of the revised welding tips and anvil fixtures, the original assembly sequence (Quarterly Progress Report No. 6, p. 12) was modified slightly to facilitate assembly of the redesigned 6080WB tube mount. This modified assembly sequence is presented in Table I. The welding sequence and the conditions for the individual steps were confirmed by the fabrication of 36 sub-assemblies prior to redelivery of the welder with associated tooling to Tung-Sol. The complete 6080WB electron-tube mount shown in Figure 3 was also fabricated.

Anvil fixture A-5, used in the final steps of the assembly sequence (snubbers to snubber support rods - Table I, steps 11A and 11B), has been modified to clamp the snubber support rod during welding. Figure 4 shows modified anvil fixture A-5. Without clamping, the alignment of the support rod is occasionally disturbed, and the rod may break through the retaining hole in the ceramic spacer, necessitating rejection of the entire tube mount. This modification was not completed in time for delivery to Tung-Sol with the new tooling on March 17, but is being completed and will be forwarded to Tung-Sol promptly after its check-out.

II. COMPONENTS WELDING

A. Tungsten-Rhenium Wire Welding

Effort on this phase of the program was curtailed because of the work involved in the redesign, fabrication, and performance check-out of tooling for the 600-watt welder.

B. Frame-Grid Welding

Sixteen wire-wound frame grids (0.003-inch gold-plated molybdenum wire wound on 0.050-inch molybdenum side rods) for preliminary welding studies were received from Tung-Sol on March 25.

Consideration of the size and configuration of the frame grids and the accurate alignment that must be maintained during welding has led to adoption of the approach of welding turns one or several at a time, rather than simultaneously welding all fifty turns required for each side of a complete frame grid. Investigation established the power range (300-600 watts) required for welding two turns simultaneously (Quarterly Progress Report No. 10); proper clamping forces for two turns are below the accurately controllable minimum attainable with standard 600-watt welding machines. An available laboratory welding system will be utilized to explore welding response within the required power range at low clamping forces (less than 70 pounds). Preparation of such a system, utilizing existing components insofar as possible, has been initiated.

Card 3/4

61227

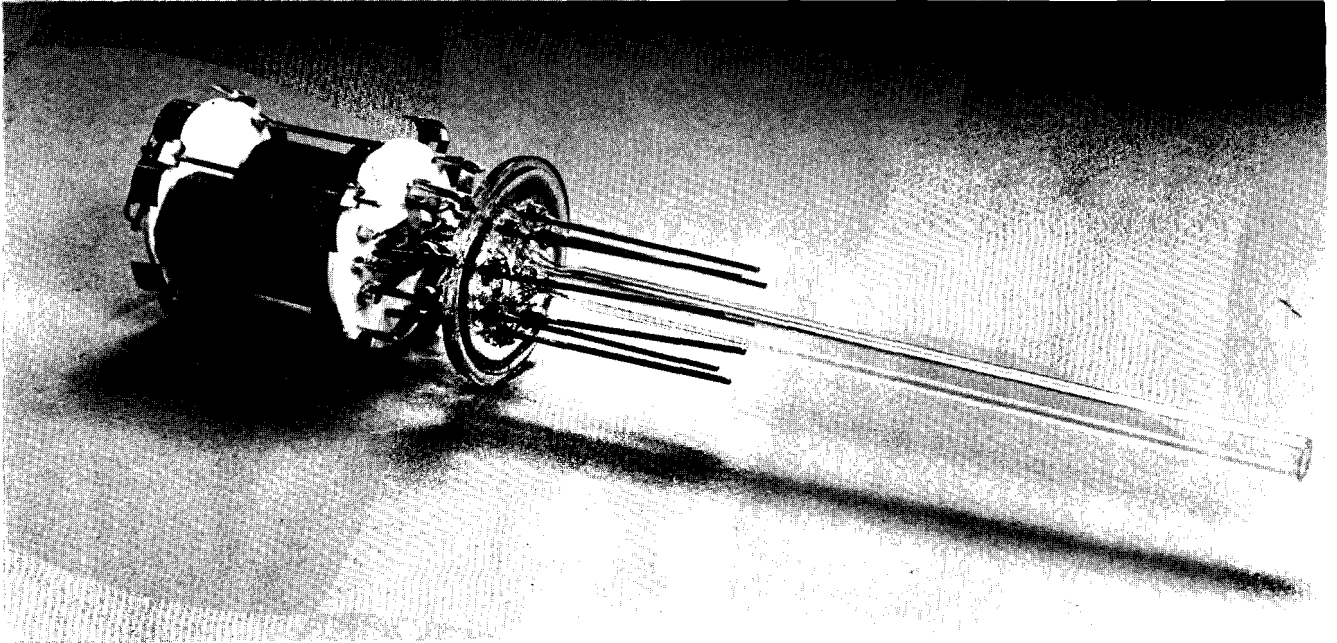


Figure 3

6080WB ELECTRON-TUBE MOUNT
WELDED WITH THE REVISED TOOLING
(Scale 1:1)

W,Mo,A

Card 4/4

61227

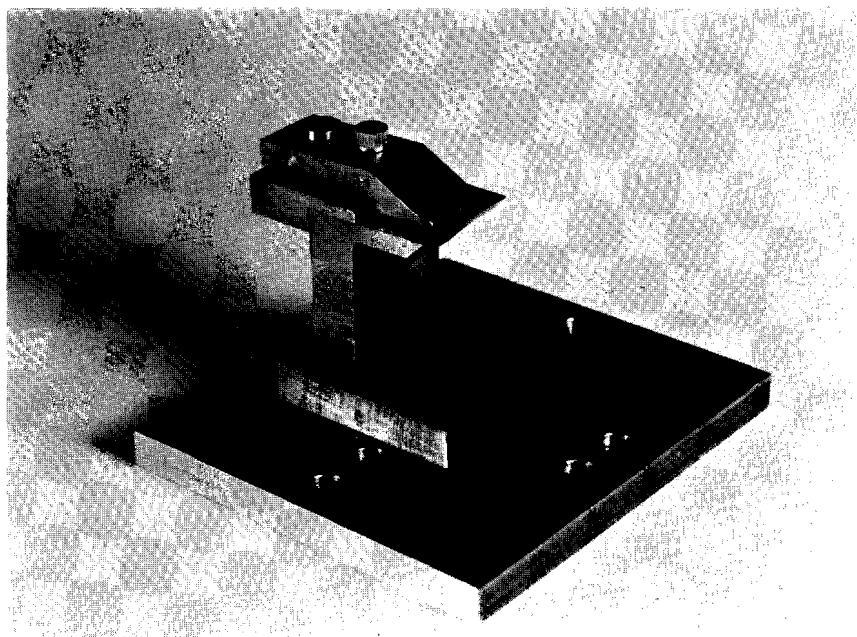


Figure 4

MODIFIED ANVIL FIXTURE A-5

W, Mo, A

Table I
ASSEMBLY SEQUENCE FOR 6080WB TUBE

<u>Sequence No.</u>	<u>Tip</u>	<u>Anvil</u>	<u>Power Setting</u>	<u>Clamping Force (lb)</u>	<u>Weld Interval (sec)</u>	<u>Operation</u>
1A	T-1	A-1	5	100	0.12	Cathode tab to cathode sleeve - 2 required
Sub-Assembly	-	-				Assemble two sleeves into top spacer
1B	T-1	A-1	2	100	0.10	Looped cathode tab to sleeve
1C	T-1	A-1	2	100	0.10	Repeat above on 2nd sleeve
Sub-Assembly	-	-				Assemble tube cage
2	T-2	A-2	0	600	0	Crimp anode eyelets to anode support rods
3A	T-2	A-2	17	200	0.10	Anode connectors (17876 17877 to anode support
3B	T-2	A-2	15	100	0.20	Weld anode eyelets to support rods
4A	T-3	A-2	5	100	0.20	Weld grid eyelets (2) to grid support
4B	T-3	A-2	6	150	0.10	Outside grid connector (17882) to grid support
Sub-Assembly	-	-				Assemble R.H. heater connector
4C	T-3	A-2	6	150	0.10	Inside grid connector (17883) to grid support
Sub-Assembly	-	-				Assemble heaters in cathode sleeve
						Insert heater wire sleeves (8)
5A	T-1	A-1	5	50	0.10	Weld alternate heater sleeves to R.H. connector

Table I (Concluded)

Sequence No.	Tip	Anvil	Power Setting	Clamping Force (lb)	Weld Interval (sec)	Operation
Sub-Assembly	-	-				Insert L.H. heater connector
5B	T-1	A-1	5	50	0.10	Weld alternate heater sleeves to L.H. connector
6A	T-4	A-4	16	100	0.20	Grid connectors to pins 1 and 4
6B	T-4	A-4	16	100	0.20	Anode connectors to pins 2 and 5 Heater connector to pins 7 and 8
6C	T-4	A-4	16	100	0.20	Cathode connectors to pins 3 and 6
7A	T-4	A-4	16	100	0.20	Snubber rod to cathode connector
7B	T-4	A-4	16	100	0.20	Snubber rod to cathode connector
8A	T-4	A-4	13	100	0.18	Top cathode connector to snubber rod
8B	T-4	A-4	13	100	0.18	Top cathode connector to snubber rod
9A	T-1	A-2	6	100	0.10	Cathode tab to cathode connector (Anvil insert inverted)
9B	T-1	A-2	6	100	0.10	Cathode tab to cathode connector (Anvil insert inverted)
10	T-6	A-6	20	100	0.1	Getter to snubber support
11A	T-5	A-5	20	150	0.35	Snubber to snubber supports
11B	T-5	A-5	20	150	0.35	Snubber to snubber supports

III. CONCLUSIONS

Fabrication of redesigned tooling for use with the 600-watt welder in fabricating 6080WB electron-tube mounts has been completed, and satisfactory welding performance has been established.

The assembly sequence has been revised to incorporate the tooling modifications. The welder and associated tooling were delivered to Tung-Sol in March, and operator training and sub-assembly welding have been initiated.

Progress on the tungsten-rhenium wire welding and frame-grid welding has been delayed by the effort required for tooling redesign and testing in connection with the welding operations at Tung-Sol.

PROGRAM FOR NEXT INTERVAL

Activity at Tung-Sol will be concentrated on fabrication of one hundred 6080WB electron tubes for age and life tests. It is anticipated that testing will be initiated during this period.

Activity of Aeroprojects will be concerned with establishing the welding conditions and tooling required for welding the frame grids. Sample welds will be examined metallographically, and joint strengths will be compared with those obtained by the gold-bonding technique presently used. Welding equipment derived from the frame-grid investigations will be used to prepare, for testing, weld samples of 0.003-inch tungsten-rhenium wire bonded to 0.060-inch sheets composed variously of tungsten, molybdenum, and nickel.

PUBLICATIONS AND REPORTS

No publications or reports were issued during this period. The following trips were made in connection with this project:

Technical consultation between Messrs. M. Yarmovsky and N. Helmstetter of Tung-Sol and Mr. J. G. Thomas of Aeroprojects was held on March 18, 1965, at Tung-Sol, Bloomfield, New Jersey.


Mr. T. A. Walraven of Aeroprojects installed the 600-watt welder on the Tung-Sol premises on March 17. On March 18 Messrs. Walraven and Thomas demonstrated the operation and assembly sequence for the Tung-Sol Operator. Messrs. Yarmovsky and Helmstetter witnessed the welding demonstrations and operator training.

Mr. Harry Shienbloom and Mr. J. G. Thomas held technical consultations and reviewed the program status on January 26 and on March 2 at USAECOM headquarters, Philadelphia, Pennsylvania.

TECHNICAL MAN-HOURS
EXPENDED DURING THIS REPORT PERIOD

<u>Aeroprojects</u>	<u>Project</u>	<u>Hours Expended During This Report Period</u>
J. G. Thomas	Project Engineer	24-1/2
T. A. Walraven	Senior Welding Technician	36
A. L. Fuchs	Chief Design Engineer	22
Engineering		102
Shop		27-1/2
	Sub Total	<u>212</u>
 <u>Tung-Sol Electric Incorporated</u>		
N. Helmstetter		<u>0</u>
	TOTAL	212

Technical surveillance of this contract is under the control of the Industrial Engineering Division, USAECOM, Philadelphia, Pennsylvania 19103. For further technical information contact Mr. Harry Shienbloom, Project Engineer (telephone number: area code 215, KI6-3200, extension 2137).

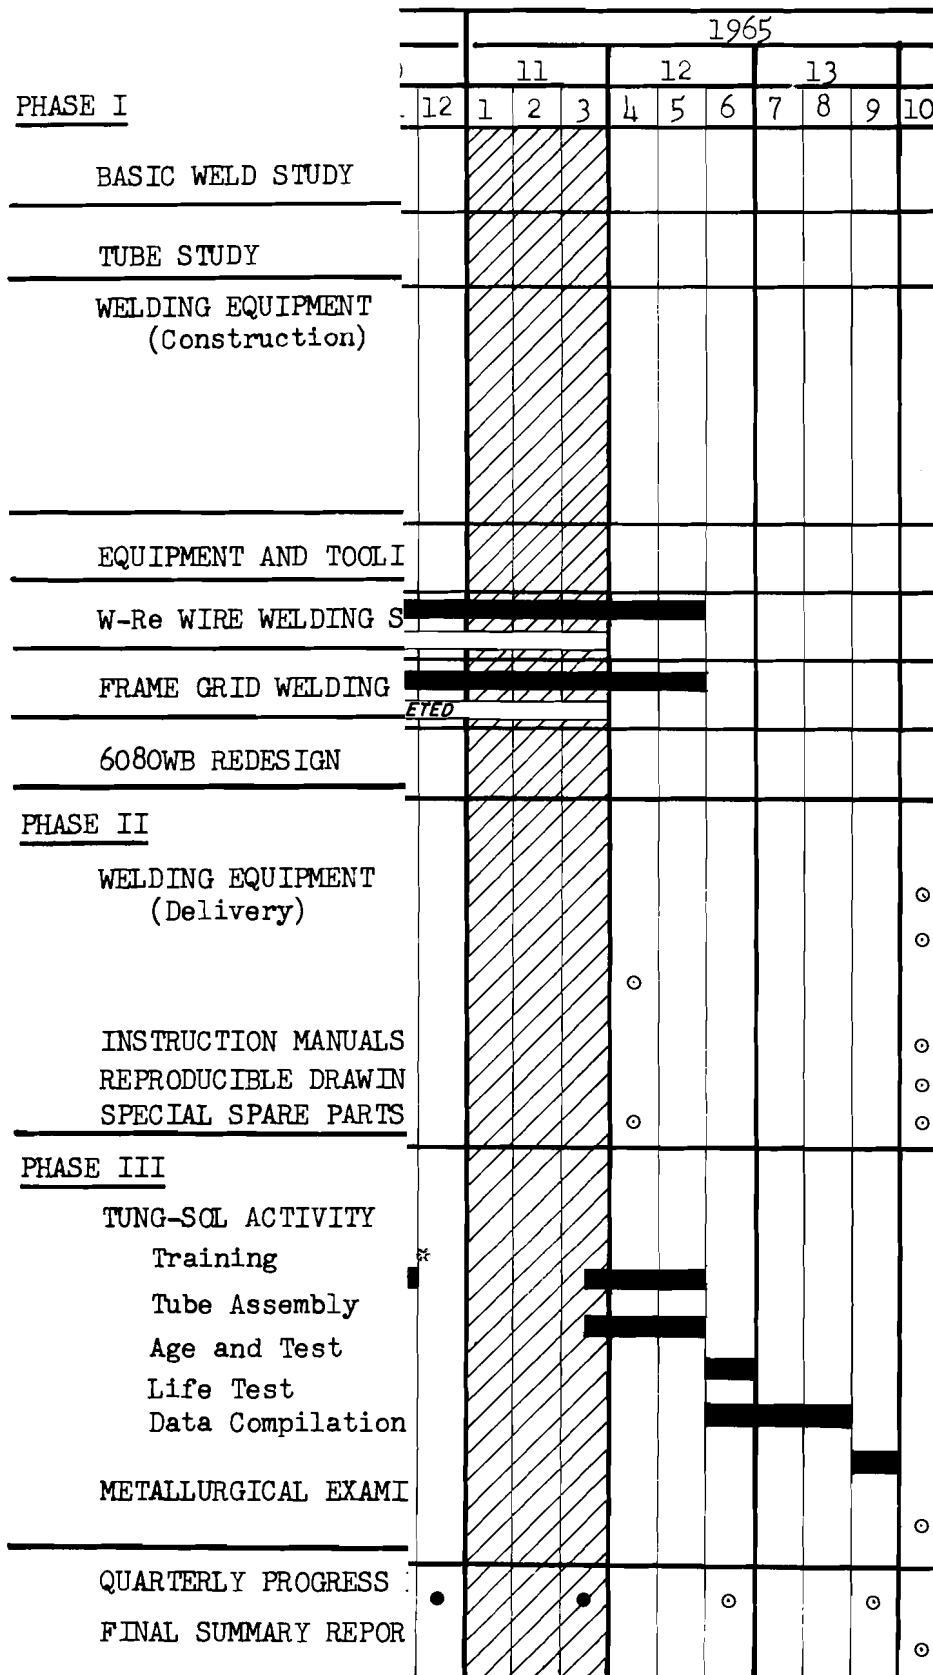

rupted during tooling revisions

LEGEND: ■ Proposed Work Study
 □ Work in Progress
 ○ Contractual Delivery
 ● Contractual Item
 ⊙ Amended Delivery

DISTRIBUTION LIST

<u>No. of Copies</u>		<u>No. of Copies</u>	
2	Advisory Group on Electron Devices 346 Broadway - 8th Floor New York, New York 10013	1	Chief, Bureau of Ships Department of the Navy Washington 25, D. C. Attn: 691A
1	Commander Aeronautical Systems Division Wright-Patterson Air Force Base Dayton, Ohio	1	Amperex Electronic Corporation 230 Duffy Avenue Hicksville, L. I., New York Attn: Mr. Alex Mitchell
3	Commanding General U. S. Army Electronics Command 225 South 18th Street Philadelphia, Pennsylvania 19103 Attn: AMSEL-PP-IED-26	1	Bell Telephone Laboratories, Inc. Technical Information Library Whippany Laboratory Whippany, New Jersey 07981
1	Commanding General U. S. Army Electronics Command Fort Monmouth, New Jersey 07703 Attn: AMSEL-PP-E-CMD-1	1	The Bendix Corporation Red Bank Division Eatontown, New Jersey Attn: Mr. Joseph F. Bozzelli
1	Director U. S. Army Electronics Laboratories Fort Monmouth, New Jersey Attn: AMSEL-RD-PR, Chief, Tube Techniques Branch	1	Bomac Laboratories, Inc. Salem Road Beverly, Massachusetts Attn: Mr. Richard S. Briggs
1	Attn: Chief, General Tubes Branch	1	Burroughs Corporation Electronic Tube Division P. O. Box 1226 Plainfield, New Jersey Attn: Mr. Roger Wolfe
1	Attn: Chief, Gaseous Electronics Section, Bldg. S-53		
10	Commander Defense Documentation Center Cameron Station Alexandria, Virginia, 22314 Attn: TISIA-1	1	Allen B. DuMont Laboratories, Inc. 750 Bloomfield Avenue Clifton, New Jersey Attn: Mr. Robert Deutsch
1	Canadian Liaison Officer Army Materiel Command Tempo 7, Room 1067 Washington, D. C. 20315	1	Edgerton, Germeshausen & Grier, Inc. Crosby Drive Bedford 15, Massachusetts 01730 Attn: Mr. S. Goldberg
1	Eitel-McCullough, Inc. 301 Industrial Way San Carlos, California Attn: Mr. H. M. Bailey		

DISTRIBUTION LIST (Continued)

<u>No. of Copies</u>		<u>No. of Copies</u>	
1	Electronic Enterprises, Inc. 65-67 Seventh Avenue Newark 4, New Jersey Attn: Mr. Richard Bloemeke	1	Lionel Electronic Laboratories, Inc. 1226 Flushing Avenue Brooklyn 37, New York
1	Electrons, Inc. 127 Sussex Avenue Newark 3, New Jersey Attn: Mr. E. K. Smith	1	Litton Engineering Laboratories P. O. Box 949 Grass Valley, California Attn: Mr. Charles V. Litton
1	General Electric Company 316 East Ninth Street Owensboro, Kentucky Attn: Mr. W. T. Millis	1	Litton Industries Electron Tube Division San Carlos, California Attn: Mr. James H. Weber
1	Gulton Industries, Inc. 212 Durham Avenue Metuchen, New Jersey Attn: Mr. Daniel Abrams	1	Machlett Laboratories, Inc. 1063 Hope Street Springdale, Connecticut Attn: Dr. H. D. Doolittle
1	Huggins Laboratories 999 East Argues Avenue Sunnyvale, California Attn: Mr. R. A. Huggins	1	Metcom, Inc. 76 Lafayette Street Salem, Massachusetts Attn: Mr. Richard Broderick
1	Hughes Aircraft Vacuum Tube Products 2020 Short Street Oceanside, California Attn: Mr. James Sutherland	1	Microwave Associates, Inc. South Street Burlington, Massachusetts Attn: Dr. L. Gould
1	International Telephone & Telegraph Corporation Electron Tube Division P. O. Box 100 Easton, Pennsylvania Attn: Mr. R. F. Mann	1	Microwave Electronics Corporation 4061 Transport Street Palo Alto, California Attn: Dr. Stanley Kaisel
		1	Ohio State University Department of Metallurgy Columbus, Ohio Attn: Mr. Frederick J. Fraikor

DISTRIBUTION LIST (Continued)

<u>No. of Copies</u>		<u>No. of Copies</u>	
1	Penta Laboratories, Inc. 312 North Nopal Street Santa Barbara, California Attn: Mr. R. L. Norton	1	Sperry Electronic Tube Division Sperry Rand Gainesville, Florida Attn: Mr. John Whitford
1	Philco Corporation Lansdale Division Church Road Attn: Mr. F. Mayock	1	Sylvania Electric Products, Inc. Emporium, Pennsylvania Attn: Mr. Vincent Grubbe
1	Polarad Electronics Corporation 43-20 Thirty-fourth Street Long Island City 1, New York Attn: Dr. D. L. Jaffe	1	Tucor, Inc. 59 Danbury Road Wilton, Connecticut Attn: Mr. R. White
1	Radio Corporation of America Electron Tube Division Lancaster, Pennsylvania Attn: Mr. Roy E. Nelson	1	Tung-Sol Electric, Inc. 200 Bloomfield Avenue Bloomfield, New Jersey Attn: Mr. Max Yarmovsky
1	Radio Corporation of America Electron Tube Division 415 South Fifth Street Harrison, New Jersey Attn: Mr. Clarence West	1	United Electronics Company 42 Spring Street Newark, New Jersey Attn: Dr. John Beers
1	Raytheon Company Spencer Lab Wayside Avenue Burlington, Massachusetts Attn: Mr. George Freedman	1	Varian Associates 611 Hansen Way Palo Alto, California Attn: Dr. Richard Nelson
1	S. F. D. Laboratories, Inc. 800 Rahway Avenue Union, New Jersey Attn: Dr. Joseph Saloom	1	The Victoreen Instrument Company 5806 Hough Avenue Cleveland 3, Ohio Attn: Mr. Ben Olson
1	Sonotone Corporation Box 200 Elmsford, New York Attn: Dr. L. G. Hector	1	Watkins-Johnson Company 3333 Hillview Avenue Palo Alto, California Attn: Dr. Rolf Peter
		1	Westinghouse Electric Corporation Electronic Tube Division Box 284 Elmira, New York Attn: Mr. B. W. Sauter

DISTRIBUTION LIST (Continued)

<u>No. of Copies</u>		<u>No. of Copies</u>	
1	U. S. Army Ordnance Frankford Arsenal Bridge & Tacony Streets Philadelphia, Pennsylvania 19137 Attn: Mr. Frank Hussey Metal Joining Section 1323, 64-1	1	Raytheon Manufacturing Company Chelmsford Street Lowell, Massachusetts Attention: Mr. W. W. Robinson
1	Battelle Memorial Institute 505 King Avenue Columbus 1, Ohio Attn: Mr. C. M. Jackson	1	Sprague Electric Company 87 Marshall Street North Adams, Massachusetts Attention: Mr. W. Bell
1	Westinghouse Electric Corporation Youngwood, Pennsylvania Attention: Mr. Ozzie Jaeger	1	Texas Instruments, Inc. Semiconductor Components Division Post Office Box 5012 Dallas 22, Texas Attention: Semiconductor Library
1	Clevite Transistor A Division of Clevite Corporation 200 Smith Street Waltham 54, Massachusetts Attention: Mr. Sam Rubinovitz	1	Transitron Electronic Corporation 168-182 Albion Street Wakefield, Massachusetts Attention: Dr. D. Bakalar
1	Rome Air Development Center Griffiss Air Force Base, New York Attention: Mr. L. Gubbins, RASGR	2	Western Electric Company Marion and Vine Streets Laureldale, Pennsylvania Attention: Mr. Robert Moore
1	Hamilton Standard Division United Aircraft Corporation Windsor Locks, Connecticut Attn: Mr. John Dudenhoefer Project Director	1	Delco Radio Division Kokomo, Indiana Attention: Dr. F. E. Jaumot, Jr.
1	Mr. C. W. Irish Marketing Section Lamp Metals & Components Dept. General Electric Company 21800 Tungsten Road Cleveland 17, Ohio	1	Bendix Corporation Semiconductor Division Holmdel, New Jersey Attention: Dr. Robert Meijer
1	Radio Corporation of America Somerville, New Jersey Attention: Mr. R. Wicks	1	Motorola, Inc. 5005 East McDowell Road Phoenix, Arizona Attention: Mr. James LaRue
		1	Pacific Semiconductors, Inc. 14520 S. Aviation Blvd. Lawndale, California Attention: Dr. H. Q. North

DISTRIBUTION LIST (Continued)

<u>No. of Copies</u>		<u>No. of Copies</u>	
1	General Electric Company Electronic Park Syracuse, New York Attention: Mr. T. F. Kendall Bldg. 7, Room 152	1	Sylvania Electric Products, Inc. Div. of General Telephone Corp. Sylvania Lighting Products Div. 60 Boston Street Salem, Massachusetts Attn: Mr. Rufus L. Briggs, Project Eng.-3C
1	Bureau of Weapons Department of the Navy Washington 25, D. C. Attention: Mr. Roy G. Gustafson RRMA-24, Materials Div.	1	ITT Industrial Laboratories 3700 East Pontiac Fort Wayne, Indiana Attn: M. F. Toohig Manager, Tubes and Sensors
1	The Rembar Company, Inc. 67 Main Street Dobbs Ferry, New York Attention: Mr. E. Dietz	1	Thermo Electron Engr. Corp. 85 First Avenue Waltham, Massachusetts Attn: Mr. T. Johnson
1	Fairchild Semiconductor Corp. 545 Whisman Road Mountain View, California Attention: Mr. Ralph Lee	1	Raytheon Company Second Avenue Waltham, Massachusetts Attn: Dr. Colin Bowness
1	Radio Corporation of America Electronic Components and Devices Lancaster, Pennsylvania Attn: Mr. Edward L. Romero	1	Raytheon Company Route 128 Burlington, Massachusetts Attn: Mr. George Freedman
1	General Electric Company Schenectady, New York Attn: Dr. Harold R. Day Building 5, Room 323	1	Ferrotec Company 217 California St. Newton, Massachusetts Attn: Mr. Paul Rutledge
1	Arinc Research Company 1700 "K" Street - NW Washington, D. C. - 20006 Attn: Mr. Robert Reed	1	IIT Research Institute 10 W. 35th Street Chicago 16, Illinois Attn: Mr. S. L. Blum

DISTRIBUTION LIST (Concluded)No. of
Copies

- 1 Electron Technology, Incorporated
626 Schuyler Avenue
Kearny, New Jersey
Attention: Mr. Stanley Koch
- 1 Eon Corporation
175 Pearl Street
Brooklyn, New York
Attention: Dr. Gustav Weinberg
- 1 National Aeronautics & Space Administration
Head, Operation Section
Scientific & Technical Information Division
(SAK/DL)
4833 Rugby Avenue
Bethesda, Maryland 20014
- 1 National Aeronautics & Space Administration
Lewis Research Center
21000 Brook Park Road
Cleveland, Ohio 44135
Attention: Mr. Davies
Mail Code: 500-309
- 1 Commanding Officer
Harry Diamond Laboratories
Washington 25, D. C.
Attention: Mr. H. G. Chandler
- 1 General Electric Co.
Pickup Tube Operation
Room 165, Bldg. 6
Electronics Park
Syracuse, N. Y.
Attn: Mr. Philip Oakes
