

AD-A089 070

TEXAS A AND M UNIV COLLEGE STATION INST OF STATISTICS

F/G 1 /5

EVALUATION OF PRECEDENCE CRITERIA FOR PROJECT SCHEDULING UNDER — TC(U)

MAY 80 S M CHANG, R L SIELKEN

N00014-78-C-0026


THEMIS-TR-63

NL

UNCLASSIFIED

For 1
Author

END
DATE
FILMED
10-80
DTIC

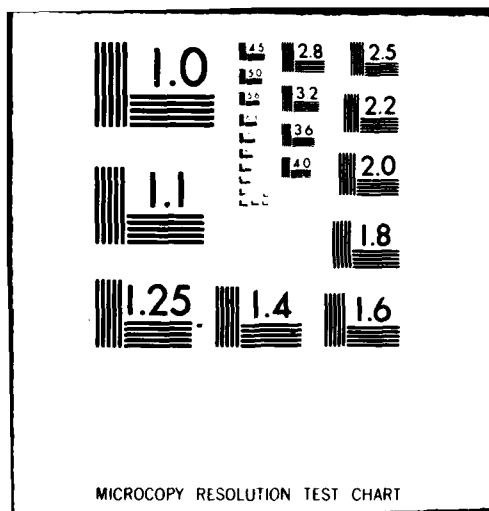

AD A089070

LEVEL

12

TEXAS A&M UNIVERSITY

COLLEGE STATION, TEXAS 77843

DTIC
ELECTE
SEP 11 1980
S C D

DDC FILE COPY.

This document has been approved
for public release and sales in
distribution is unlimited.

THEMIS

80 1 10 054

12

TEXAS A&M UNIVERSITY
PROJECT THEMIS

Technical Report #63

EVALUATION OF PRECEDENCE CRITERIA FOR PROJECT
SCHEDULING UNDER RESOURCE CONSTRAINTS

by

Shi Min Chang and Robert L. Sielken, Jr.

DTIC
ELECTE
SEP 11 1980
S C D

Texas A&M University
Office of Naval Research
Contract N00014-78-C-0426
Project NR047-179

Reproduction in whole or in part
is permitted for any purpose of
the United States Government

This document has been approved
for public release and sale;
its distribution is unlimited

ATTACHMENT I

EVALUATION OF PRECEDENCE CRITERIA FOR PROJECT
SCHEDULING UNDER RESOURCE CONSTRAINTS

by

Shi Min Chang and Robert L. Sielken, Jr.

THEMIS OPTIMIZATION RESEARCH PROGRAM
Technical Report No. 63
May, 1980

INSTITUTE OF STATISTICS
Texas A&M University

Research conducted through the
Texas A&M Research Foundation
and sponsored by the
Office of Naval Research
Contract N00014-78-C-0426
Project NR047-179

Reproduction in whole or in part
is permitted for any purpose of
the United States Government.

This document has been approved
for public release and sale; its
distribution is unlimited.

ATTACHMENT II

ABSTRACT

When more than one activity in a project requires the same indivisible resource, the project schedule can resolve this resource constraint by specifying the order in which these activities are to be performed. Several heuristic criteria for determining this order are considered. The minimum cost schedule for a given project deadline can often be found by determining the optimal schedule ignoring the resource constraints and then resolving any resource usage conflicts by ordering the conflicting activities so as to minimize the project completion time. A simple procedure for determining this latter order is given.

Accession For	
NTIS Grant	☒
DDC TAB	☐
Unannounced	☐
Justification	
By _____	
Distribution/	
Availability Codes	
Dist	Avail and/or special
A	

Table of Contents

	Page
1. Introduction	1
2. The Problem	4
3. A Heuristic Procedure Based on Precedence Relationship	8
4. Testing the Precedence Criteria in the Heuristic Procedure	11
5. Checking the Usefulness of the Five Criteria	32
6. An "Easy" Way to Implement Criterion 4	34
7. Concluding Remarks	36
References	38

List of Figures

	Page
Figure 1: Project Network	1
Figure 2: Activity Cost vs. Activity Mean Duration	4
Figure 3: Activity Cost vs. Activity Mean Duration for Activity B	5
Figure 4: The Time Duration Intervals for Competing Activities	9
Figure 5: Original Project Network for P_1	12
Figure 6: Restructured Project Network for $3 \rightarrow 4 \rightarrow 5$	15
Figure 7: Restructured Project Network for $3 \rightarrow 5 \rightarrow 4$	17
Figure 8: Restructured Project Network for $4 \rightarrow 5 \rightarrow 3$	18
Figure 9: Restructured Project Network for $4 \rightarrow 3 \rightarrow 5$	20
Figure 10: Restructured Project Network for $5 \rightarrow 4 \rightarrow 3$	21
Figure 11: Restructured Project Network for $5 \rightarrow 3 \rightarrow 4$	23
Figure 12: Project Network for P_2	26
Figure 13: Project Network for P_3	29

List of Tables

	Page
Table 1: Activity Mean Durations	2
Table 2: Activity Costs and Durations for Project P_1	13
Table 3: Optimal Project Schedules for Two Specified Deadline Times Ignoring Resource Constraints for Project P_1	14
Table 4: Optimal Schedule for $3 \rightarrow 4 \rightarrow 5$	16
Table 5: Optimal Schedule for $3 \rightarrow 5 \rightarrow 4$	17
Table 6: Optimal Schedule for $4 \rightarrow 5 \rightarrow 3$	19
Table 7: Optimal Schedule for $4 \rightarrow 3 \rightarrow 5$	20
Table 8: Optimal Schedule for $5 \rightarrow 4 \rightarrow 3$	22
Table 9: Optimal Schedule for $5 \rightarrow 3 \rightarrow 4$	23
Table 10: Precedence Relationships and Project Costs Corresponding to Precedence Criteria (1) - (5) . . .	24
Table 11: Activity Costs and Durations for P_2	26
Table 12: Optimal Project Schedule for P_2 Ignoring Resource Constraints (Project Deadline = 14.)	27
Table 13: Precedence Relationship and Project Cost Corresponding to Criteria (1) - (5) When Activity 2 and 3 Conflict and Project Deadline is 14 in P_2 . . .	27
Table 14: Precedence Relationship and Project Cost Corresponding to Criteria (1) - (5) When Activity 4 and 5 Conflict and Project Deadline is 14 in P_2 . . .	28
Table 15: Activity Costs and Duration for P_3	30
Table 16: Optimal Project Schedule for P_3 Ignoring Resource Constraint (Project Deadline = 30.)	30
Table 17: Precedence Relationship and Project Cost Corresponding to Criteria (1) - (5) When Activity 3 and Activity 4 Conflict and Project Deadline is 30 in P_3	31

	Page
Table 18: Precedence Relationship and Project Cost Corresponding to Criteria (1) - (5) When Activity 4 and Activity 5 Conflict and Project Deadline is 30 in P_3	31
Table 19: The Usefulness of the Precedence Criteria in the Three Experimental Projects	32
Table 20: Comparing the Project Schedules for a Project Deadline of 14	33

I. Introduction.

Usually project scheduling techniques consider the project as a network of activities. In the project network an activity can be represented by a branch (arrow) between two nodes (circles). Nodes represent the beginnings and/or completions of activities. For example, the network for a project consisting of activities A, B, C, D, E, F, and G is given in Figure 1.

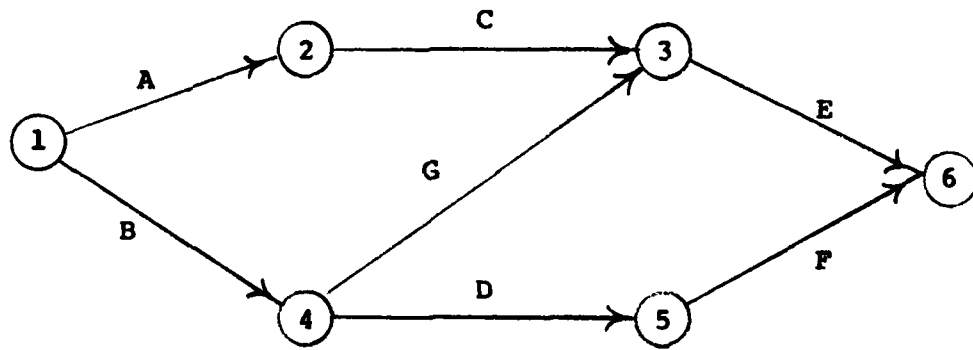


Figure 1. Project Network

The node numbers within the circles are for reference purposes only.

In Figure 1, these six activities have the following relationships:

- (i) A and B start at the same time.
- (ii) A must be completed before C can be started; and C and G must be completed before E can be started.

B must be completed before D and G can be started;
 and D must be completed before F can be started.
 That is, A precedes C, C precedes E, B precedes D,
 B precedes G, G precedes E, and D precedes F.

- (iii) The project will not be finished until both E and F are completed

The time that it actually takes to complete an activity from beginning to end is called the activity's duration and may be a random variable. The mean duration of each activity has been determined for this example and they are given in Table 1.

Table 1. Activity Mean Durations.

<u>Activity</u>	<u>Mean Duration</u>
A	10 hours
B	12 hours
C	8 hours
D	7 hours
E	11 hours
F	9 hours
G	0 hours

The overall project duration has been calculated as the maximum path length where a path length is calculated by the addition of all activity durations along the path. When each activity duration is its mean, the path through

A-C-E takes twenty-eight hours, the path through B-G-E takes twenty-three hours, the path through B-D-F takes twenty-nine hours, and the critical (longest) path is through B-D-E taking twenty-nine hours.

The cost of an activity is assumed to be a convex piecewise linear function of the activity's mean duration. This allows for the possibility that an activity duration can sometimes be shortened by the application of greater amounts of resources such as labor and capital. This implies that the expenditure of more money may reduce the duration of an activity. There is, therefore, a time/cost trade-off for each activity in the project and an overall trade-off involving project duration and project expense. For example, in Figure 2 to have a duration in the interval of $[T_1, T_2]$ might be more expensive than $[T_2, T_3]$ due to the use of more efficient equipment.

A project schedule is a specification of each activity's mean duration. The time to complete the project is a random variable whose distribution depends on the activity duration distributions. The objective is to determine a minimum cost project schedule such that the mean of the corresponding project completion time distribution is less than or equal to a specified project deadline.

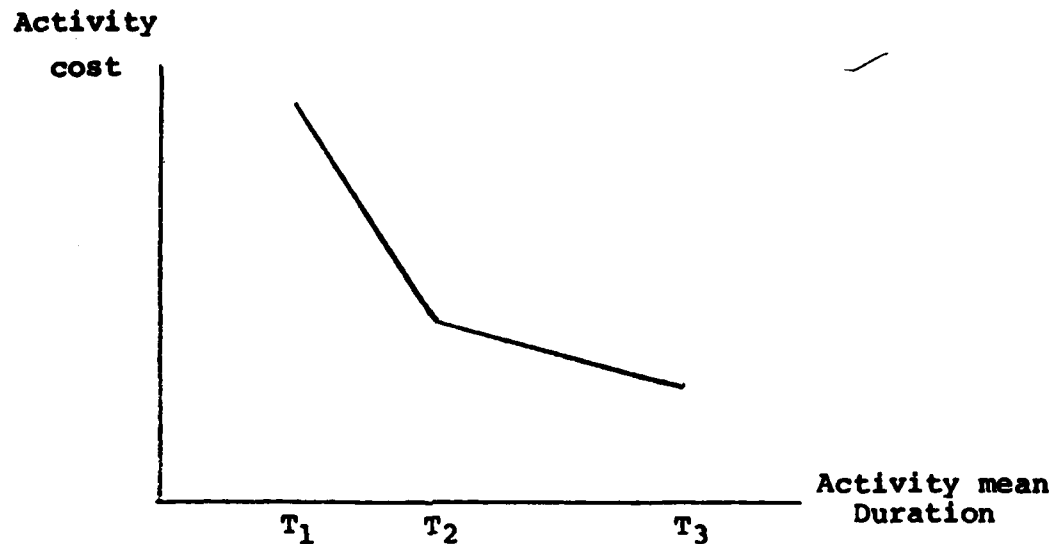


Figure 2. Activity Cost vs. Activity Mean Duration

2. The Problem.

In project scheduling, there are two kinds of feasibility constraints commonly found. First, there are limits on the amount of available resources. Second, there are restrictions on the order in which tasks can be performed. A solution to a project scheduling must be a feasible resolution to both of these two types of constraints. The resolution of the problem of limited resources requires answers to two kinds of questions:

1. Which resources will be allocated to which tasks?
2. When will each activity be performed?

In other words, without the assumption of unlimited

resources one must make both allocation decisions and precedence decisions.

For example, in a shipyard there may be only one large capacity crane. Activity A cannot be performed without the crane. The relationship between the mean completion time for activity B, say T_B , and its cost is as in Figure 3.

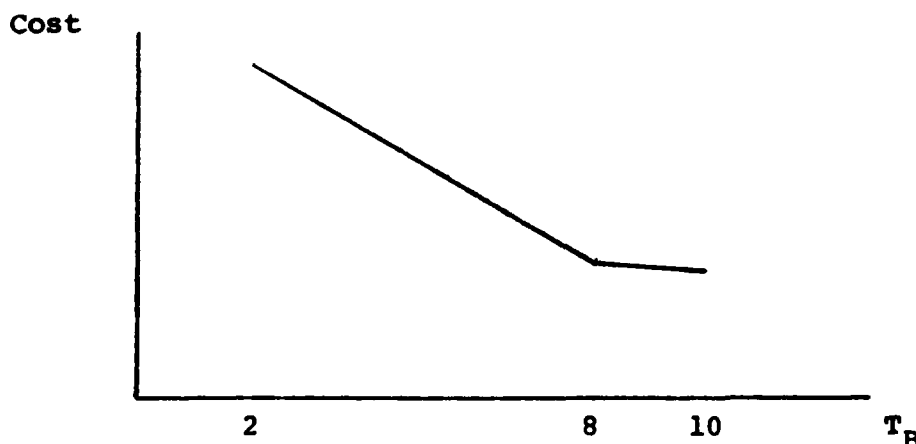


Figure 3. Activity Cost vs. Activity Mean Duration for Activity B

If $2 \leq T_B \leq 8$, the crane must be used for activity B. If $8 \leq T_B \leq 10$, an alternative less expensive procedure not involving the crane is used. Let Start A and Start B be the times at which activities A and B are scheduled to begin. Let T_A (T_B) be the mean duration scheduled for activity A (B). Then there are three possibilities:

1. The time interval [Start A, Start A + T_A] and [Start B, Start B + T_B] do not overlap;
2. the time intervals do overlap but $T_B \geq 8$; and

3. the time intervals overlap and $T_B < 8$.

Only the third possibility causes difficulties for activity A and activity B compete for using the crane.

When we try to resolve the limited resources problem, two reasons stand out as the causes for the current uncertainty and lack of a definitive solution to these problems.

The first difficulty is the statement of the problem. Often times, only a subset of the resources are required for the full duration of the activity; the other resources are needed only for a fraction of that duration. The analyst must then choose between subdividing the activity according to the combination of resources required at any point of time, which may lead to a prohibitively complicated network, or leaving the activity as an entity--a course of action that must lead to a gross exaggeration of the total requirements. Furthermore, it is generally recognized that the time estimates of an activity duration are based on subjective knowledge of the availability of resources. The functional relationship between these two variables may not be known, but it in no sense vitiates its existence. It follows that subdividing the activity in accord with its resources requirement at various points of time may change the time estimates of the subdivisions, which in turn may affect the resource requirement. A vicious cycle results

which may disrupt any possibility of obtaining meaningful results.

Another major roadblock to a clear and precise statement of the problem is the fact that an activity can be started and possibly maintained for a long time, with fewer resources than are ideally needed. If the functional relationship between resource availability and the duration were known, analysis similar to the time-cost trade-off analysis could be conducted. But in general, this functional relationship is not defined. Moreover, activities that require more than one resource would require a complete different treatment from those activities requiring only one resource.

The second reason stems from difficulties in the formulation of the mathematical model. There is the interdependence among the activities due to the sharing of the same resources and the dependence of resource consumption on the manner in which the activity is subdivided. Both of these dependencies are basically nonlinear in character. Thus even if the functional relationship describing the dependencies were determined there would still remain the task of combining these individual relations into a meaningful whole.

Furthermore it is often difficult to ascertain the objectives of management, particularly when these

objectives are poorly formulated and far from crystallized in management's own mind. For example, the objective may be any one of the following three:

1. Minimize total project cost assuming unlimited availability of the various resources at a price. The price may or may not be linear with the quantity ordered.
2. Minimize the duration of the project under limited availability of resources.
3. Level the resource consumption while meeting a specified project completion deadline.

3. A Heuristic Procedure Based on Precedence Relationship.

If the minimum cost schedule is determined, the situation might be as Figure 4 where activities A, B, and C compete for the same critical resource.

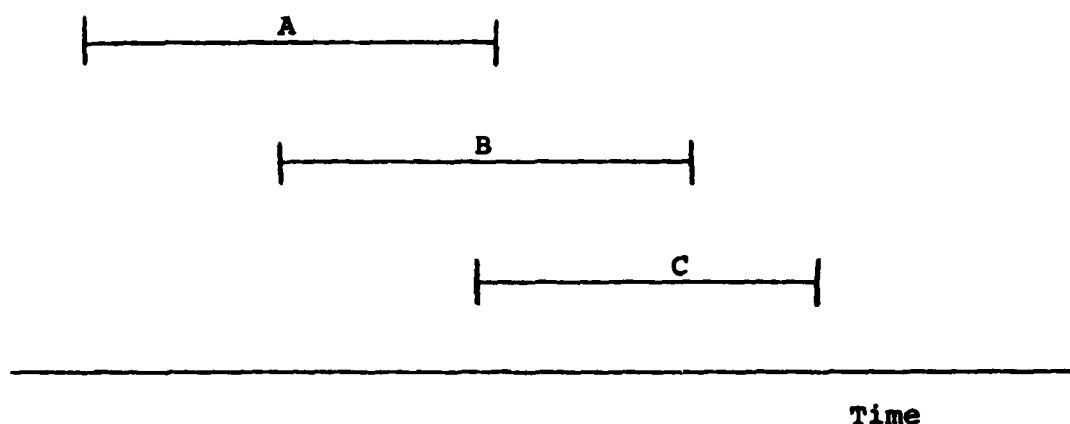


Figure 4. The Time Duration Intervals for Competing Activities

One way to resolve the resource conflict is through required precedence relationships. What we have to do is determine some way of deciding what the precedence relationship among these activities should be; say A before B before C, or B before A before C, etc. There are several reasonable ways of deciding these precedence relationships. For example, one might say that A should start before B if in the current infeasible project schedule

1. activity A started before activity B;
2. the midpoint of the duration interval for activity A was less than that for activity B;
3. activity A finished before activity B;
4. doing activity A before activity B increased the project completion time less than doing activity B before activity A.

5. the cost of decreasing the mean completion time for activity A is less than the corresponding cost for activity B.

Once a precedence relationship among the competing activities has been determined, the project network can be redrawn and a new minimum cost schedule determined.

The whole heuristic procedure to mediate the competition for limited resources by using precedence relationships can be outlined as follows:

Step (1) Determine the minimum cost schedule for the project network disregarding resource constraints. This can be done using the network-flow algorithm described in Technical Report #55 if each activity's duration is assumed to equal its mean duration. Alternatively, it can be done using the Statistical PERT algorithm described in Technical Report #57 if the randomness of each activity's duration is to be explicitly considered.

Step (2) Examine the current project scheduling. If there are no resource conflicts go to Step 4. Otherwise, select a criterion from (1) - (5) as mentioned above for establishing the precedence relationships and determine the precedence relationship associated with each conflict.

Step (3) Redraw the project network to reflect any new precedence relationships. Dummy activities having zero duration and cost may have to be introduced to preserve the original inter-activity relationships. Return to Step 1.

Step (4) An "optimal" schedule which does not violate the resource constraints has been found.

4. Testing the Precedence Criteria in the Heuristic Procedure.

Since it is impractical to redraw the project network and to explicitly evaluate each precedence criterion (1) - (5) for each project network, the objective is to find guidelines for choosing a precedence criterion which usually provides a near minimum total project cost subject to a specified project deadline and limited critical resources.

To evaluate the precedence criteria (1) - (5), several sample projects have been considered. The first project (P_1) is described in Table 2 and depicted in Figure 5. In Table 2 the activity cost as a convex piecewise linear function of the mean duration is implied by the given time and costs at the ends of the linear segments.

The optimal project schedules (apart from resource constraints) for project deadlines of 39 and 35 are given in Table 3 for project P_1 .

Figure 5. Original Project Network for P_1

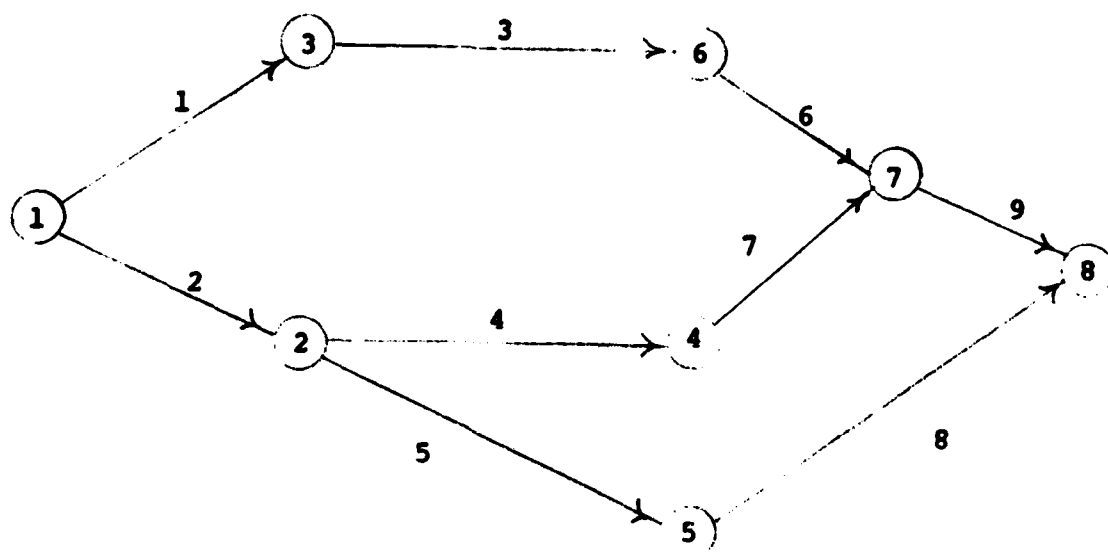


Table 2. Activity Costs and Durations for Project P₁

Activity Number	Origin Node	Terminal Node	Number of Different Completion Times	Time and Cost	Segments		
1	1	3	2	time cost	4 8	6 5	
2	1	2	3	time cost	3 9	5 6	9 3
3	3	6	3	time cost	8 15	12 10	15 8
4	2	4	3	time cost	5 9	8 5	10 3
5	2	5	3	time cost	4 10	6 6	10 3
6	6	7	2	time cost	5 6	8 4	
7	4	7	3	time cost	4 8	6 5	7 4
8	5	8	2	time cost	10 8	15 4	
9	7	8	2	time cost	7 8	10 4	

**Table 3. Optimal Project Schedules
for Two Specified Deadline Times Ignoring
Resource Constraints for Project P_1**

Activity Number	Project Deadline		Project Deadline	
	39		35	
	Activity	Activity	Activity	Activity
	Duration	Cost	Duration	Cost
1	6	5	6	5
2	9	3	9	3
3	15	8	12	10
4	10	3	10	3
5	10	3	10	3
6	8	4	8	4
7	7	4	7	4
8	15	4	15	4
9	10	4	9	5.33
Project Cost		38	41.33	

Suppose that in P_1 activities 3, 4, and 5 compete for the same resources. In what follows the effect on the project cost of using the precedence criteria (1) - (5) to resolve the resources conflict is evaluated.

First, we consider the precedence relationship to be activity 3 before activity 4 before activity 5, ($3 \rightarrow 4 \rightarrow 5$), where " $\rightarrow$ " implies "precedes". The corresponding project network is in Figure 6. Activity 10 is a dummy activity with zero duration and zero cost. The corresponding optimal schedules are given in Table 4.

Figure 6. Restructured Project Network for $3 \rightarrow 4 \rightarrow 5$

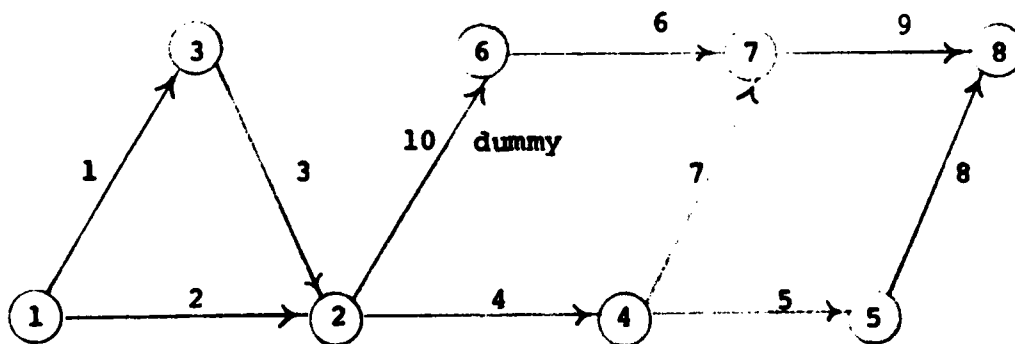


Table 4. Optimal Schedule for 3 → 4 → 5

Activity Number	Project Deadline		Project Deadline	
	39		35	
	Activity	Activity	Activity	Activity
	Duration	Cost	Duration	Cost
1	6	5	5	6.5
2	9	3	9	3
3	8	15	8	15
4	8	5	5	9
5	6	6	6	6
6	8	4	8	4
7	7	4	7	4
8	11	7.2	11	7.2
9	10	4	10	4
10	0	0	0	0
Project Cost		53.2	58.7	

Second, we consider the precedence relationship activity 3 before activity 5 before activity 4. The corresponding project network and optimal schedules are in Figure 7 and Table 5 respectively.

Figure 7. Restructured Project Network for 3 + 5 + 4

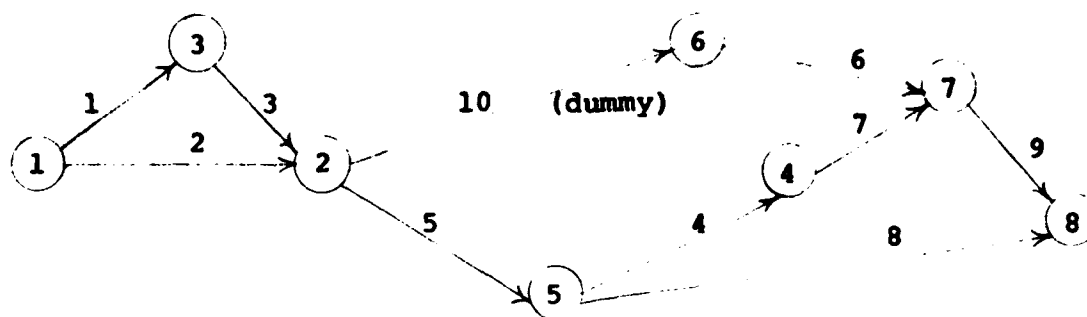


Table 5. Optimal Schedule for 3 + 5 + 4

Activity Number	Project Deadline 39		Project Deadline 35	
	Activity Duration	Activity Cost	Activity Duration	Activity Cost
1	6	5	4	8
2	9	3	9	3
3	8	15	8	15
4	5	9	5	9
5	6	6	6	6
6	8	4	8	4
7	6	5	5	6.5
8	15	4	15	4
9	8	6.67	7	8
10	0	0	0	0
Project Cost		57.67	63.5	

Third, we consider the precedence relationship activity 4 before activity 5 before activity 3. The corresponding project network and optimal schedule are in Figure 8 and Table 6 respectively.

Figure 8. Restructured Project Network for $4 \rightarrow 5 \rightarrow 3$

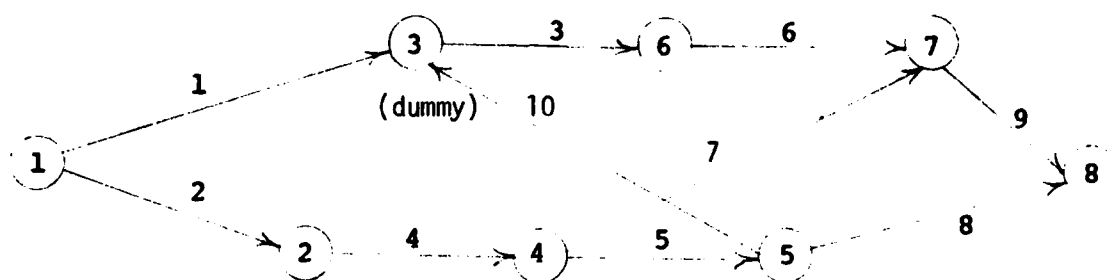


Table 6. Optimal Schedule for 4 → 5 → 3

Activity Number	Project Deadline		Project Deadline	
	39		35	
	Activity	Activity	Activity	Activity
	Duration	Cost	Duration	Cost
1	6	5	6	5
2	5	6	4	7.5
3	8	15	8	15
4	5	9	5	9
5	6	6	6	6
6	5	6	5	6
7	7	4	7	4
8	15	4	15	4
9	10	4	7	8
10	0	0	0	0
Project Cost		59	64.5	

Fourth, we consider the precedence relationship activity 4 before activity 3 before activity 5. The corresponding project network and optimal schedule are in Figure 9 and Table 7 respectively.

Figure 9. Restructured Project Network for 4 + 3 + 5

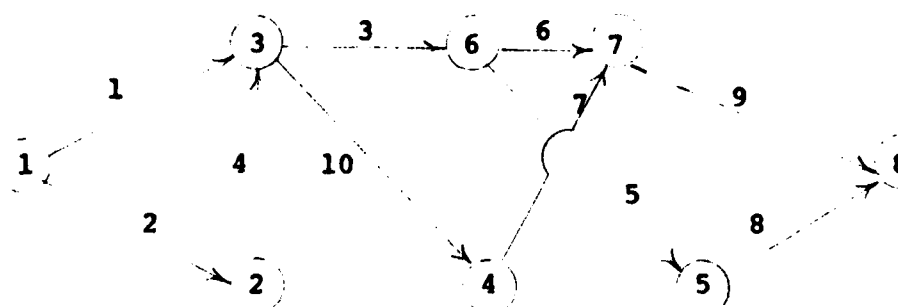


Table 7. Optimal Schedule for 4 + 3 + 5

Activity Number	Project Deadline		Project Deadline	
	39		35	
	Activity	Activity	Activity	Activity
	Duration	Cost	Duration	Cost
1	6	5	6	5
2	5	6	5	6
3	8	15	8	15
4	8	5	5	9
5	6	6	6	6
6	8	4	7	4.67
7	7	4	7	4
8	12	6.4	11	7.2
9	10	4	10	4
10	0	0	0	0
Project Cost		55.4	60.87	

Fifth, we consider the precedence relationship activity 5 before activity 4 before activity 3. The corresponding project network and optimal schedule are in Figure 10 and Table 8 respectively.

Figure 10. Restructured Project Network for $5 \rightarrow 4 \rightarrow 3$

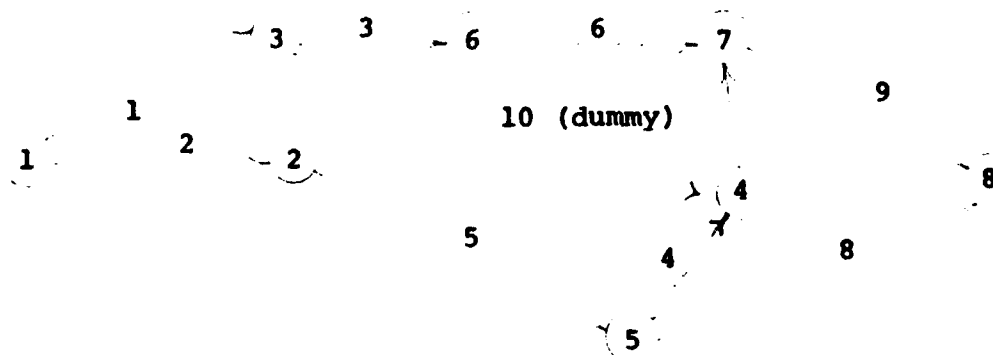


Table 8. Optimal Schedule for 5 → 4 → 3

Activity Number	Project Deadline		Project Deadline	
	39		35	
	Activity	Activity	Activity	Activity
	Duration	Cost	Duration	Cost
1	6	5	6	5
2	5	6	4	7.5
3	8	15	8	15
4	5	9	5	9
5	6	6	6	6
6	5	6	5	6
7	7	4	7	4
8	15	4	15	4
9	10	4	7	8
10	0	0	0	0
Project Cost		59	64.5	

Sixth, we consider the precedence relationship activity 5 before activity 3 before activity 4. The corresponding project network and optimal schedule are in Figure 11 and Table 9 respectively.

Figure 11. Restructured Project Network for 5 + 3 + 4

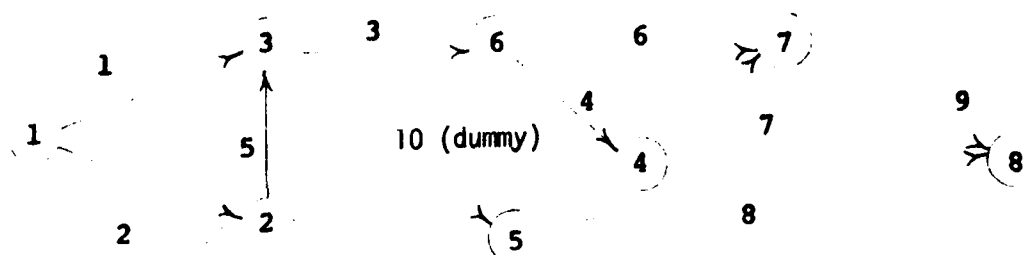


Table 9. Optimal Schedule for 5 + 3 + 4

Activity Number	Project Deadline 39		Project Deadline 35	
	Activity	Activity	Activity	Activity
	Duration	Cost	Duration	Cost
1	6	5	6	5
2	5	6	3	9
3	8	15	8	15
4	5	9	5	9
5	6	6	6	6
6	8	4	8	4
7	6	5	6	5
8	15	4	15	4
9	9	5.33	7	8
10	0	0	0	0
Project Cost		59.33	65	

Table 10 indicates the precedence relationship for project P_1 corresponding to each of the precedence criteria (1) - (5). If a criterion implies two possible precedence relationships, both are listed in Table 10.

Table 10. Precedence Relationships and Project Costs Corresponding to Precedence Criteria (1) - (5).

Project Deadline	Criteria	Precedence Relationship	Project Cost
39	1	3 → 4 → 5	53.20
		3 → 5 → 4	57.67
	2	3 → 4 → 5	53.20
		3 → 5 → 4	57.67
	3	5 → 4 → 3	59
		4 → 5 → 3	59
	4	3 → 4 → 5	53.2
		4 → 5 → 3	59
	5	5 → 4 → 3	59.33
35	1	3 → 4 → 5	58.7
		3 → 5 → 4	63.5
	2	5 → 4 → 3	64.5
		4 → 5 → 3	64.5
	3	3 → 4 → 5	58.7
		3 → 5 → 4	63.5
	4	3 → 4 → 5	58.7
		4 → 5 → 3	64.5
	5	5 → 4 → 3	64.5

When the precedence relationships implied by the criteria are compared to the optimal precedence relation (determined by complete enumeration of the possible precedence relations, Figure 6 - Figure 11 and Table 4 - 9), we find that using criterion 1, 2, and 4 provide the optimal project cost when the project deadline is 39, and criterion 1, 3, and 4 provide the optimal project cost when deadline is 35.

A second sample project network P_2 is depicted in Figure 12 and described in Table 11. The project deadline is assumed to be 14. The optimal schedule (ignoring resource constraints) is given in Table 12.

Assume that activity 2 and activity 3 compete for the same critical resource. An evaluation of the five precedence criteria is summarized in Table 13. In Table 13 the optimal project cost is 36 corresponding to using criteria 2, 3, or 4. Also assume that activity 4 and activity 5 compete for the same critical resources. The resolution of the conflict of activity 4 and activity 5 by the five precedence criteria is summarized in Table 14. In Table 14 the optimal project cost is 43 corresponding to using criteria 3 or 5.

**Table 12. Optimal Project Schedule for P_2
Ignoring Resource Constraints
(Project Deadline = 14.)**

Activity Number	Activity Duration	Activity Cost
1	3	8
2	4	8
3	3	6.75
4	7	2
5	8	7
Project Cost		31.75

**Table 13. Precedence Relationship and Project
Cost Corresponding to Criteria (1) - (5) When
Activity 2 and 3 Conflict and Project Deadline
is 14 in P_2**

Criteria	Precedence Relationship	Project Cost
1	2 → 3	39
	3 → 2	36
2	3 → 2	36
3	3 → 2	36
4	3 → 2	36
5	2 → 3	39

Table 14. Precedence Relationship and Project Cost Corresponding to Criteria (1) - (5) When Activity 4 and 5 Conflict and Project Deadline is 14 in P_7

Criteria	Precedence Relationship	Project Cost
1	5 $\rightarrow$ 4	45
2	5 $\rightarrow$ 4	45
3	5 $\rightarrow$ 4	45
	4 $\rightarrow$ 5	43
4	5 $\rightarrow$ 4	45
5	4 $\rightarrow$ 5	43

The third sample project network P_3 is depicted in Figure 13 and described in Table 15. If the project completion time is 30, the optimal project schedule (ignoring resources constraints) is given in Table 16.

Assume that activity 3 and activity 4 compete for the same critical resource. An evaluation of the five precedence criteria is summarized in Table 17. In Table 17, the optimal project cost is 20.67 corresponding to criteria 1, 2, and 4 when the project deadline is 30.

Assume that activity 4 and activity 5 compete for the same critical resources. The results of the resolution of

the resource conflict between activity 4 and activity 5 by the five precedence criteria are given in Table 18. In Table 18 the optimal project cost is 46 corresponding to criteria 1, 2, 3, 4, and 5 when project deadline is 30.

Figure 13. Project Network for P_3

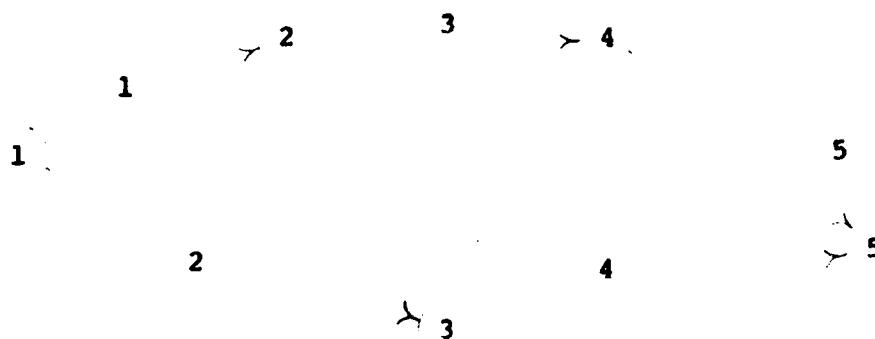


Table 15. Activity Costs and Duration for P_3

Activity Number	Origin Node	Terminal Node	Number of Different Completion Times	Time and Cost	Segments			
1	1	2	2	time cost	3 8	7 3		
2	1	3	3	time cost	4 16	8 8	12 4	
3	2	4	4	time cost	5 16	8 10	10 6	16 4
4	3	5	2	time cost	4 10	7 5		9
5	4	5	3	time cost	3 12	6 8	4	

Table 16. Optimal Project Schedule for P_3
Ignoring Resource Constraint
(Project Deadline = 30.)

Activity Number	Activity Duration	Activity Cost
1	7	3
2	12	4
3	14	4.3
4	7	5
5	9	4

Table 17: Precedence Relationship and Project Cost
Corresponding to Criteria (1) - (5) When Activity 3
and Activity 4 Conflict and Project Deadline is 30 in P_3

Criteria	Precedence Relationship	Project Cost
1	3 → 4	20.67
2	3 → 4	20.67
3	4 → 3	30
4	3 → 4	20.67
5	4 → 3	30

Table 18: Precedence Relationship and Project Cost
Corresponding to Criteria (1) - (5) When Activity 4
and Activity 5 Conflict and Project Deadline is 30 in P_3

Criteria	Precedence Relationship	Project Cost
1	4 → 5	46
2	4 → 5	46
3	4 → 5	46
4	4 → 5	46
5	4 → 5	46

5. Checking the Usefulness of the Five Criteria

The usefulness of the precedence criteria in the six cases arising in the three experimental projects is given in Table 19.

Table 19. The Usefulness of the Precedence Criteria in the Three Experimental Projects*

Project Number		P_1		P_2		P_3	
Conflicting Activities		3,4,5	3,4,5	2,3	4,5	3,4	4,5
Project Deadline		39	35	14	14	30	30
Criteria	1	X	X			X	X
	2	X		X		X	X
	3		X	X	X		X
	4	X	X	X		X	X
	5				X		X

* the "X" denotes the criterion which yielded the minimum cost precedence relationship.

From Table 19 it is apparent that several criteria often yield the minimum cost schedule. However, criterion 4 which corresponds to ordering the conflicting activities so as to minimize the project completion time is most frequently optimal, 5 out of 6 cases. The optimal activity

durations related to the one case in which criterion 4 failed are given in Table 20. From Table 20 it is apparent that in the one case where criteria 4 failed it did so because an activity, 3, not involved in the resource conflict had to have its duration substantially reduced (cost substantially increased) under the schedule corresponding to criterion 4 but not under the alternative schedule.

Table 20. Comparing the Project Schedules
for a Project Deadline of 14

Activity	Original Schedule		Schedules Including Resource Constraint			
			Criterion 4:		Other:	
			5 → 4		4 → 5	
	Time	Cost	Time	Cost	Time	Cost
1	3*	8	3*	8	3*	8
2	4	8	4	8	4*	8
3	3*	6.75	2*	8	6	3
4	7	2	5*	6	3*	9
5	8*	7	4*	15	4*	15
Total		31.75		45		43

*the time for an activity on the critical path

6. An "Easy" Way to Implement Criterion 4

Initially each activity's mean duration is chosen ignoring the resource constraints. If activities A and B have a resource conflict under this schedule, then criterion 4 implies that A should precede B, $A \rightarrow B$, if, for these original activity mean durations, the schedule with $A \rightarrow B$ has a smaller project completion time than the schedule with $B \rightarrow A$. The remainder of this section describes a relatively easy procedure for determining which activity order corresponds to the smaller project completion time for given activity mean durations.

The simplest case is when only activities, say A and B, compete for the same critical resource. The restructured network with $A \rightarrow B$ will have smaller project completion time if

$$O_A + T_B < O_B + T_A$$

where

O_i = the length of the longest path from the source to the origin node of activity i,
and

T_i = the length of the longest path from the terminal node of activity i to the sink.

For example in the experimental project P_3 activities 3 and 4 compete for the same resource.

There

$$O_3 = 7 = \text{duration of activity 1};$$

$$O_4 = 12 = \text{duration of activity 2};$$

$T_3 = 9$ - duration of activity 5;

$T_4 = 0$, since the terminal node of activity 4 is the sink.

Hence

$$O_3 + T_4 = 7 + 0 = 7 < O_4 + T_3 = 12 + 9 = 23$$

and activity 3 should precede activity 4. With the activity durations at their means and activity 3 preceding activity 4 the critical path contains activities 1, 3, and 5 and has completion time 30. With $4 \rightarrow 3$ the critical path contains 2, 3, 4, and 5 and has completion time 42.

For the more complicated situation where more than two activities compete for the same critical resource. We can use a similar strategy. Let activities A B and C compete for the same critical resource. If

$$O_A = \text{Min. } \{O_A, O_B, O_C\}$$

$$T_B = \text{Min. } \{T_A, T_B, T_C\} ,$$

then the project completion time is minimized when $A \rightarrow C \rightarrow B$. If

$$O_A = \text{Min } \{O_A, O_B, O_C\}$$

$$T_A = \text{Min } \{T_A, T_B, T_C\} ,$$

then we have to find $\text{Min } \{O_B, O_C\}$ and $\text{Min } \{T_B, T_C\}$, say O_B and T_C respectively. Then we find $\text{Min } \{O_A + T_C, O_B + T_A\}$. If $O_B + T_A$ is the minimum, then $B \rightarrow C \rightarrow A$ leads to a minimum project completion time. If $O_A + T_C$ is the minimum, then $A \rightarrow B \rightarrow C$ leads to a minimum project completion time.

For example in experimental project P_1 activities 3, 4 and 5 compete for the same critical resource when

project deadline is 39. Here

$$O_3 = 6 = \text{duration of activity 1;}$$

$$O_4 = 9 = \text{duration of activity 2;}$$

$$O_5 = 9 = \text{duration of activity 2;}$$

$$O_3 = \text{Min } \{O_3, O_4, O_5\};$$

$$T_3 = 16 = \text{duration of activities 6 and 9;}$$

$$T_4 = 17 = \text{duration of activities 7 and 9;}$$

$$T_5 = 15 = \text{duration of activity 8;}$$

$$T_5 = \text{Min } \{T_3, T_4, T_5\}.$$

Hence $3 \rightarrow 4 \rightarrow 5$ leads to the minimum project completion time. In fact, checking all six possible precedence relations, we have the following:

precedence relation:	project completion time:
$3 \rightarrow 4 \rightarrow 5$	56
$3 \rightarrow 5 \rightarrow 4$	58
$4 \rightarrow 5 \rightarrow 3$	62
$4 \rightarrow 3 \rightarrow 5$	59
$5 \rightarrow 4 \rightarrow 3$	62
$5 \rightarrow 3 \rightarrow 4$	61 .

7. Concluding Remarks

When more than one activity in a project requires the same indivisible resource, the project schedule can resolve this resource constraint by specifying the order in which

these activities are to be performed. Five heuristic criteria for determining this order have been considered. Although each criterion was sometimes useful, the minimum cost schedule for a given project deadline was most frequently found by determining the optimal schedule ignoring the resource constraints and then resolving any resource usage conflict by ordering the conflicting activities so as to minimize the project completion time.

This latter precedence criterion does not always yield a minimum cost schedule. This happens because the criterion chooses the activity ordering corresponding to the minimum project completion time for given activity mean durations and does not consider the cost of compressing this project completion time to meet a specified project deadline. The difficulty arises because the derivative of the activity cost with respect to the activity duration is not the same for all activities. Hence it may cost less to shorten one network's completion time by 5 units than to shorten another by 3 units.

REFERENCES

Baker, T. C. Jr. and R. L. Sielken Jr., "A User's Guide to the Computer Implementation of the New Project Scheduling Procedure : Statistical PERT", THEMIS Project Technical Report No. 57, August, 1978.

Dunn, C. S. and R. L. Sielken Jr., "Statistical PERT : An Improved Project Scheduling Algorithm", THEMIS Project Technical Report No. 55, February, 1977.

Unclassified

SECURITY CLASSIFICATION OF THIS PAGE (When Data Entered)

REPORT DOCUMENTATION PAGE		READ INSTRUCTIONS BEFORE COMPLETING FORM
1. REPORT NUMBER 63	2. GOVT ACCESSION NO. AD-A089 070	3. RECIPIENT'S CATALOG NUMBER
4. TITLE (and Subtitle) EVALUATION OF PRECEDENCE CRITERIA FOR PROJECT SCHEDULING UNDER RESOURCE CONSTRAINTS.		5. TYPE OF REPORT & SERIES COVERED Technical rept.
7. AUTHOR(s) Shi Min Chang and Robert L. Sielken, Jr.		6. PERFORMING ORG. REPORT NUMBER
9. PERFORMING ORGANIZATION NAME AND ADDRESS Texas A&M University Institute of Statistics College Station, TX 77843		8. CONTRACT OR GRANT NUMBER(s) N00014-78-C-0426
11. CONTROLLING OFFICE NAME AND ADDRESS		10. PROGRAM ELEMENT, PROJECT, TASK AREA & WORK UNIT NUMBERS NR 047-179
14. MONITORING AGENCY NAME & ADDRESS (if different from Controlling Office) Office of Naval Research		12. REPORT DATE May 1980
		13. NUMBER OF PAGES 45
		15. SECURITY CLASS. (of this report) Unclassified
		15a. DECLASSIFICATION/DOWNGRADING SCHEDULE
16. DISTRIBUTION STATEMENT (of this Report) Approved for public release; distribution unlimited. THEMIS-TK-63		
17. DISTRIBUTION STATEMENT (of the abstract entered in Block 20, if different from Report) NA		
18. SUPPLEMENTARY NOTES		
19. KEY WORDS (Continue on reverse side if necessary and identify by block number) project scheduling resource constraints random activity durations choosing activity duration distributions		
20. ABSTRACT (Continue on reverse side if necessary and identify by block number) When more than one activity in a project requires the same indivisible resource, the project schedule can resolve this resource constraint by specifying the order in which these activities are to be performed. Several heuristic criteria for determining this order are considered. The minimum cost schedule for a given project deadline can often be found by determining the optimal schedule ignoring the resource		

DD FORM 1 JAN 73 1473

EDITION OF 1 NOV 68 IS OBSOLETE
S/N 0102-LF-014-6601

Unclassified

SECURITY CLASSIFICATION OF THIS PAGE (When Data Entered)

347380

JTB

Unclassified

SECURITY CLASSIFICATION OF THIS PAGE (When Data Entered)

19. cont.

competition for indivisible resources
minimum cost schedule
project completion time distribution
specified project deadline
statistical PERT

20. cont.

→ constraints and then resolving any resource usage conflicts by ordering the conflicting activities so as to minimize the project completion time. A simple procedure for determining this latter order is given.

Unclassified

SECURITY CLASSIFICATION OF THIS PAGE(When Data Entered)

6 April 1979

BASIC DISTRIBUTION LIST FOR
UNCLASSIFIED TECHNICAL REPORTS
OPERATIONS RESEARCH PROGRAM
ONR CODE 434

Operations Reserach Program (Code 434)	(3)	Professor Gerald L. Thompson	(1)
Office of Naval Research		Graduate School of Industrial Adm.	
Arlington, VA 22217		Carnegie-Mellon University	
		Pittsburgh, PA 15213	
Defense Technical Information Center	(12)	Professor George B. Dantzig	(1)
Cameron Station		Department of Operations Research	
Alexandria, VA 22314		Stanford University	
Defense Logistics Studies	(1)	Stanford, CA 94305	
Information Exchange		Professor Ronald W. Shephard	(1)
Army Logistics Management Center		Operations Research Center	
Fort Lee, VA 23801		University of California	
Office of Naval Research Branch Office	(1)	Berkeley, CA 94720	
New York Area Office		Mr. Harvey Paige	(1)
715 Broadway - 5th Floor		Maritime Transportation Research Board	
New York, NY 10003		National Academy of Sciences	
Office of Naval Research Branch Office	(1)	Washington, D.C. 20418	
Bldg. 114, Section D		Professor William F. Lucas	(1)
666 Summer Street		Department of Operations Research	
Boston, MA 02210		Cornell University	
Office of Naval Research Branch Office	(1)	Ithaca, NY 14850	
1030 East Green Street		Professor Arthur M. Geoffrion	(1)
Pasadena, CA 91106		Graduate School of Business Adm.	
	(1)	University of California	
		Los Angeles, CA 90024	
Office of Naval Research Branch Office	(1)	Dr. Richard Hatch	(1)
536 South Clark Street		Decision Systems Associates, Inc.	
Chicago, IL 60605		350 Fortune Terrace, 2nd Floor	
Professor Martin Shubik	(1)	Rockville, MD 20854	
Department of Economics		Professor H. Donald Ratliff	(1)
Yale University		School of Industrial &	
New Haven, CT 06520		Systems Engineering	
		Georgia Institute of Technology	
Professor Abraham Charnes	(1)	Atlanta, GA 30332	
Department of Mathematics		Professor Robert M. Stark	(1)
The University of Texas		Department of Statistics &	
Austin, TX 78712		Computer Sciences	
		University of Delaware	
		Newark, DE 19711	

Professor George S. Fishman
Curriculum in Operations Research
& Systems Analysis
University of North Carolina
Chapel Hill, NC 27514

Prof. Harvey M. Wagner
School of Business Administration
University of North Carolina
Chapel Hill, NC 27514

The George Washington University
Logistics Research Project
707 22nd Street, N.W.
Washington, D.C. 20037

Professor Averill M. Law
Department of Industrial Engineering
University of Wisconsin
Madison, WI 53706

Professor Marshall Fisher
Decision Sciences Department
The Wharton School
University of Pennsylvania
Philadelphia, PA 19174

Dr. George E. Pugh
Decision-Science Applications, Inc.
1500 Wilson Blvd.
Arlington, VA 22209

Professor Harvey M. Salkin
Department of Operations Research
Case Western Reserve University
Cleveland, OH 44106

Professor Darwin Klingman
Department of Operations Research
& Computer Sciences
University of Texas
Austin, TX 78765

(1) Professor Douglas Montgomery (1)
School of Industrial & Systems Eng.
Georgia Institute of Technology
Atlanta, GA 30332

(1) Dr. R. L. Sielken (1)
Institute of Statistics
Texas A&M University
College Station, TX 77843

(1)

(1) Dr. Joseph Augusta (1)
MATHTECH, Inc.
1401 Wilson Boulevard
Arlington, VA 22209

Professor Gerald J. Lieberman (1)
Department of Operations Research
Stanford University
Stanford, CA 94305

(1) Professor Cyrus Derman (1)
Department of Civil Engineering
and Engineering Mechanics
Columbia University
New York, NY 10027

(1) Professor K. T. Wallenius (1)
Department of Mathematical Sciences
Clemson University
Clemson, SC 29631

(1) Professor M. L. Shooman (1)
Department of Electrical Engineering
Polytechnic Institute of New York
Brooklyn, NY 11201

(1) Dr. Nancy Mann (1)
Rockwell International Corporation
Science Center
P.O. Box 1085
Thousand Oaks, CA 91360

Professor Wallace R. Blischke
Dept. of Quantitative Business Analysis
University of Southern California
Los Angeles, CA 90007

Professor R. S. Leavenworth
Department of Industrial
& Systems Engineering
University of Florida
Gainesville, FL 32611

Professor M. Zia Hassan
Department of Industrial &
Systems Engineering
Illinois Institute of Technology
Chicago, IL 60616

Dr. Paul Arvis
DRXMC-PRO
Army Logistics Management Center
Fort Lee, VA 23801

LCOL Daniel E. Strayer, USAF
Executive Director
Air Force Business Research
Management Center/LAPB
Wright-Patterson AFB, OH 45433

Mr. L. G. LaMarca
Program Director for Sea Control
Studies, Code 127
Naval Weapons Center
China Lake, CA 93555

Dr. Wilhelm Bortels
Naval Underwater Systems Center (Code 214)
New London, CT 06320

Dr. Glen E. Hornbaker
Armaments Development Department
Naval Surface Weapons Center
Dahlgren, VA 22448

Mr. Charles M. Merrow
Operations Analysis Group (Code 121B)
Naval Ocean Systems Center
San Diego, CA 92152

(1) Mr. Thomas E. Willey (1)
Chief of Planning, Systems Analysis
& Engineering Department
Naval Air Development Center
Warminster, PA 18974

(1) Mr. Ted C. Buckley (1)
Analysis & Intelligence Office (Code 530)
Naval Coastal Systems Laboratory
Panama City, FL 32401

(1) Mr. Marshall J. Tino (1)
Ordnance Systems Assessment Division
Naval Surface Weapons Center
White Oak
Silver Spring, MD 20910

(1) Mr. Russell Richards (1)
Naval Postgraduate School (Code 55)
Monterey, CA 93940

(1) Naval Postgraduate School (1)
Department of Operations Research
Monterey, CA 93940

(1) Naval Postgraduate School (1)
Library (Code 0212)
Monterey, CA 93940

(1) Dr. A. L. Slafkosky (1)
Scientific Advisory
Commandant Marine Corps (Code AX)
Washington, D.C. 20380

(1) Assistant Chief for Technology (1)
Office of Naval Research, Code 200
Arlington, VA 22217

(1) Dr. Joseph Bram (1)
Directorate of Mathematical
& Information Sciences
Air Force Office of Scientific Research/F
Bolling Air Force Base
Washington, D.C. 20032

(1) Applied Mathematics Laboratory (1)
Attn: Mr. Gene Gleissner
Naval Ship Research & Development Center
Washington, D.C. 20007

Army War College (1)
Attn: Library
Carlisle Barracks, PA 17013

Naval War College (1)
Attn: Library
Newport, RI 02840

Captain R. E. Helmes, Jr. (1)
Naval Operations (Code 964)
Pentagon 4A538
Washington, D.C. 20350

Dr. Paul Boggs (1)
U.S. Army Research Office
P.O. Box 12211
Research Triangle Park, NC 27709

Professor Stephen E. Jacobsen (1)
Department of System Science
School of Engineering &
Applied Science
University of California
Los Angeles, CA 90024
