



EXCERPT FROM THE PROCEEDINGS

OF THE SEVENTH ANNUAL ACQUISITION RESEARCH SYMPOSIUM WEDNESDAY SESSIONS VOLUME I

**Acquisition Research
Creating Synergy for Informed Change
May 12 - 13, 2010**

Published: 30 April 2010

Approved for public release, distribution unlimited.

Prepared for: Naval Postgraduate School, Monterey, California 93943



Report Documentation Page		Form Approved OMB No. 0704-0188
Public reporting burden for the collection of information is estimated to average 1 hour per response, including the time for reviewing instructions, searching existing data sources, gathering and maintaining the data needed, and completing and reviewing the collection of information. Send comments regarding this burden estimate or any other aspect of this collection of information, including suggestions for reducing this burden, to Washington Headquarters Services, Directorate for Information Operations and Reports, 1215 Jefferson Davis Highway, Suite 1204, Arlington VA 22202-4302. Respondents should be aware that notwithstanding any other provision of law, no person shall be subject to a penalty for failing to comply with a collection of information if it does not display a currently valid OMB control number.		
1. REPORT DATE MAY 2010	2. REPORT TYPE	3. DATES COVERED 00-00-2010 to 00-00-2010
4. TITLE AND SUBTITLE Cost-Benefit Study of a Project to Lower Cost and Improve Fleet Readiness through Integrating the Management of Technical Information		5a. CONTRACT NUMBER
		5b. GRANT NUMBER
		5c. PROGRAM ELEMENT NUMBER
6. AUTHOR(S)	5d. PROJECT NUMBER	
	5e. TASK NUMBER	
	5f. WORK UNIT NUMBER	
7. PERFORMING ORGANIZATION NAME(S) AND ADDRESS(ES) Institute for Defense Analyses,4850 Mark Center Drive,Alexandria,VA,22311-1882		8. PERFORMING ORGANIZATION REPORT NUMBER
9. SPONSORING/MONITORING AGENCY NAME(S) AND ADDRESS(ES)		10. SPONSOR/MONITOR'S ACRONYM(S)
		11. SPONSOR/MONITOR'S REPORT NUMBER(S)
12. DISTRIBUTION/AVAILABILITY STATEMENT Approved for public release; distribution unlimited		
13. SUPPLEMENTARY NOTES 7th Annual Acquisition Research Symposium to be held May 12-13, 2010 in Monterey, California. U.S. Government or Federal Rights License		

14. ABSTRACT

This paper describes a cost-benefit analysis by the Institute for Defense Analyses of the ?Bridge Project? that ADL (Advanced Distributed Learning) is conducting for the Office of Secretary of Defense for Acquisition, Technology and Logistics (OSD(AT&L) to improve the management of Integrated Logistics Support (ILS). The Project is part of the OSD RTOC program (Reduction in Total Ownership Cost). The Bridge Project focuses on integrating (Bridging) the management and production of technical manuals and training courses. The benefits would be lower cost to produce these manuals and courses in the future, and improved readiness through insuring the delivery of consistent and up-to-date logistics support to the Fleet. Manuals and courses are currently produced by entirely separate processes. Tech writers and course developers obtain contractor data on systems and equipments in parallel they express the information in different formats, they organize the data in different structures, and they store the data in different repositories. Cost is therefore higher because of duplication of resources and the difficulties in re-using data. The lack of integration can also reduce readiness, since it opens up the possibility that the tech manuals and training courses present disparate information, thus depriving ship operators and maintainers of the most effective support. The Bridge Project seeks to relieve these problems by designing new software technical and business processes to integrate the production of technical manuals and training courses. All technical and learning content would be expressed by the same digital specification (the S1000D industry specification), they would employ the same structure (Data Modules), and the data would all be stored in the same repositories (Common Source Data Bases, or CSDBs). The project is developing an API (Application Programming Interface) to enable course developers to exchange data with any CSDB, and a Web Service to more quickly update tech manuals and training courses in response to Engineering Change Proposals (ECPs). The analysis finds that the Bridge would achieve net benefits (benefits less costs) of approximately \$87 million over 10 years, far more than enough to cover the \$8.7 million 10- year cost of producing all Navy HM&E (Hull, Mechanical and Electrical) technical manuals and training courses delivered by Navy e-Learning, a part of the Naval Education and Training Command (NETC). A sensitivity analysis of the most uncertain inputs yields a range of results (net benefits) from \$32 million to \$166 million. The Bridge could also contribute to shipboard readiness by insuring the Navy?s policy of providing up-to-date and

15. SUBJECT TERMS

16. SECURITY CLASSIFICATION OF:

a. REPORT
unclassified

b. ABSTRACT
unclassified

c. THIS PAGE
unclassified

17. LIMITATION OF
ABSTRACT
**Same as
Report (SAR)**

18. NUMBER
OF PAGES
27

19a. NAME OF
RESPONSIBLE PERSON

The research presented at the symposium was supported by the Acquisition Chair of the Graduate School of Business & Public Policy at the Naval Postgraduate School.

To request Defense Acquisition Research or to become a research sponsor, please contact:

NPS Acquisition Research Program
Attn: James B. Greene, RADM, USN, (Ret.)
Acquisition Chair
Graduate School of Business and Public Policy
Naval Postgraduate School
555 Dyer Road, Room 332
Monterey, CA 93943-5103
Tel: (831) 656-2092
Fax: (831) 656-2253
E-mail: jbgreene@nps.edu

Copies of the Acquisition Sponsored Research Reports may be printed from our website
www.acquisitionresearch.net



Cost-Benefit Study of a Project to Lower Cost and Improve Fleet Readiness through Integrating the Management of Technical Information

Dan Levine— Dr. Dan Levine holds a PhD in physics and an MA in economics. After a time at Harry Diamond Labs and the National Bureau of Standards, he has been working since 1962 on economics and cost-effectiveness studies at the Center for Naval Analyses and the Institute for Defense Analyses. His areas of research have been in Navy and Army logistics, and a variety of areas in OSD planning. Levine gives the lecture on cost effectiveness analysis for the course in cost analysis that the IDA Cost Analysis and Research Division gives annually to graduate students in operations research at George Mason University.

Abstract

This paper describes a cost-benefit analysis by the Institute for Defense Analyses of the “Bridge Project” that ADL (Advanced Distributed Learning) is conducting for the Office of Secretary of Defense for Acquisition, Technology and Logistics (OSD(AT&L) to improve the management of Integrated Logistics Support (ILS). The Project is part of the OSD RTOC program (Reduction in Total Ownership Cost). The Bridge Project focuses on integrating (Bridging) the management and production of technical manuals and training courses. The benefits would be lower cost to produce these manuals and courses in the future, and improved readiness through insuring the delivery of consistent and up-to-date logistics support to the Fleet.

Manuals and courses are currently produced by entirely separate processes. Tech writers and course developers obtain contractor data on systems and equipments in parallel, they express the information in different formats, they organize the data in different structures, and they store the data in different repositories. Cost is therefore higher because of duplication of resources and the difficulties in re-using data. The lack of integration can also reduce readiness, since it opens up the possibility that the tech manuals and training courses present disparate information, thus depriving ship operators and maintainers of the most effective support.

The Bridge Project seeks to relieve these problems by designing new software, technical and business processes to integrate the production of technical manuals and training courses. All technical and learning content would be expressed by the same digital specification (the S1000D industry specification), they would employ the same structure (Data Modules), and the data would all be stored in the same repositories (Common Source Data Bases, or CSDBs). The project is developing an API (Application Programming Interface) to enable course developers to exchange data with any CSDB, and a Web Service to more quickly update tech manuals and training courses in response to Engineering Change Proposals (ECPs).

The analysis finds that the Bridge would achieve net benefits (benefits less costs) of approximately \$87 million over 10 years, far more than enough to cover the \$8.7 million 10-year cost of producing all Navy HM&E (Hull, Mechanical and Electrical) technical manuals and training courses delivered by Navy e-Learning, a part of the Naval Education and



Training Command (NETC). A sensitivity analysis of the most uncertain inputs yields a range of results (net benefits) from \$32 million to \$166 million.

The Bridge could also contribute to shipboard readiness by insuring the Navy's policy of providing up-to-date and consistent information to the Fleet upon installation of new systems and equipment. A parametric analysis indicates that by increasing the availability of the electronic, ordnance and HM&E components of a single new DDG 1000 destroyer for only a single day would increase effectiveness the Navy values at \$2 million.

Executive Summary

The Institute for Defense Analyses (IDA) is conducting a cost-benefit analysis of the "Bridge Project" that the Advanced Distributed Learning (ADL) office is conducting for the Office of the Secretary of Defense for Acquisition, Technology and Logistics (OSD(AT&L)). The project is part of OSD's RTOC program (Reduction in Total Ownership Cost). The project's focus is on improving how the Navy manages several aspects of Integrated Logistics Support (ILS) in order to reduce the cost of producing technical manuals and training courses. A related benefit is increasing readiness through insuring the Navy's policy of having the appropriate logistics support on hand when new systems and equipment upgrades are fielded.

Under current ILS management, manuals and courses are produced by entirely separate processes. Tech writers and course developers obtain contractor data on new systems and equipment upgrades in parallel. They express the data in different formats, they organize the data in different structures, and they store the data in different repositories. The cost of producing logistics support is therefore higher because of the duplication of resources and the difficulties in re-using data. The lack of integration can also reduce readiness, since it opens up the possibility that the tech manuals and training courses present disparate information. And there may be delays in updating the information in response to Engineering Change Proposals (ECPs). These disparities and delays can deprive ship operators and maintainers of the most up-to-date information on their systems and equipment.

The Bridge project is designing a new process—new software, technical and business processes to integrate ("Bridge") the production of technical manuals and training courses. The initial beneficiary of the funding is the Littoral Combat Ship (LCS) Mission Modules Program (PMS 420), which is integrating the Mission Modules into the LCS. Under the Bridge Project, all technical and learning content would be expressed by the same digital specification (the S1000D industry specification), organized by the same structure (Data Modules), and stored in the same repositories (Common Source Data Bases). The project is also developing an Application Programming Interface (API) to grant all course developers access to any CSDB, and a Web Service to quickly identify the technical and learning content that must be reviewed for updating in response to Engineering Change Proposals (ECPs).

The cost-benefit study estimates the investment and implementation costs of designing and implementing the integrated approach. Investment is measured by the personnel and related expenses of the project during the second, or coming year of this 2-year project. (The first-year costs are sunk, and no longer relevant.) Implementation involves training technical writers and course developers in using the Bridge, and the licenses and user fees to cover the additional costs of maintaining the networks and the data repositories.



The Bridge Project's benefits are the anticipated reduction in the costs of producing future technical manuals and training courses, and possible improvements in shipboard readiness.

The cost savings were estimated by first listing the dozens of tasks (38 for the manual and 80 for the courses) to produce a nominal 500-page technical manual and a nominal one-content-hour training course. Project personnel estimated the number of staff hours to produce these tasks under both current and Bridge processes, and thus the staff hour savings from using the Bridge. Pay rates are used to convert the staff hour savings to cost savings. The final step is scaling up the results to the sample of yearly production of technical manuals and training courses. Costs and benefits were expressed in 10-year present values calculated using the 2.4% annual discount rate mandated by OMB for 10-year studies.

Two different samples were chosen for analysis, reflecting the different perspectives of OSD and the PMS 420 Program Office. The first analysis recognizes OSD's interest in seeing whether the new software and technical and business processes that comprise the Bridge would lead to positive net benefits to DoD overall—would the benefits cover the costs if implemented by the Navy and other Services as a whole. This analysis is therefore conducted for a substantial number of the Navy's yearly production of technical manuals and training courses: all Hull, Mechanical, and Electrical (HM&E) technical manuals produced by the Naval Ship System Engineering Station (NAVSSSES) in Philadelphia (over 45,000 pages annually), and 50% of the Computer-Based Training (CBT) courses delivered by Navy e-Learning (NeL), a part of the Naval Education and Training Command (NETC) (approximately 3,300 content hours annually, in total).

Only 50% of the NeL courses were considered because our analysis of the course titles indicated that only half of the courses trained "hard skills." These are the training courses that deal with equipment and other technical content, and whose cost would therefore be reduced by integrating the production of training courses and technical manuals. (Although courses that train "soft skills" such as leadership and personal advancement would not be directly affected by integration, they might benefit from the information-organizing features of the other Bridge innovations.)

The second analysis, reflecting the Program Office's perspective, is a test case of the results of the aggregate analysis in which the Bridge is applied to a particular system, the LCS's AN/AQS-20A mine hunting sonar. The focus here is on the benefits alone—whether the Bridge would lead to reductions in future cost of producing future technical manuals and training courses for this system. It would not be reasonable to expect the benefits for a single program to cover the full investment and implementation costs of the Bridge, which could lead to savings across DoD.

The first analysis finds that the Bridge would save approximately \$87 million in 10 year cost in producing the Navy HM&E manuals and 50% of NeL delivered courses—far more than enough to cover the \$8.7 million investment and implementation costs of the program. The second analysis finds that the Bridge would produce substantial savings of almost \$306 thousand in producing technical manuals and training courses for the LCS AN/AQS-20A.

Dealing with uncertainty was a major analytical problem. Although much of the analysis used historical data from NAVSSSES, NETC and the AN/AQS-20A program, the cost savings are also based on several uncertain inputs relating to the new Bridge process. A sensitivity analysis was conducted of five inputs: 1) the future pay rate for technical writers and course developers who are trained in using the Bridge, 2) the percentage of training



hours that would be benefited by the Bridge, 3) the investment cost (to hedge against unanticipated cost of developing the Bridge), 4) the implementation cost (to hedge against problems caused by the cultural changes in Navy programming), and 5) the percentage saving in course developer staff hours from using the Bridge. Considering these changes in combination yielded a full range of net benefits (benefits less costs) for the aggregate case varying from a minimum of \$32 million to the Base Case of \$78 million (\$87 million less \$8.7 million) to a maximum of \$160 million. Efforts will be taken in the second year of this study to further refine the inputs.

There is every reason to expect that net benefits would be significantly larger if the Bridge were applied to all Navy manuals and courses, and those of the other Services as well.

The final benefit for analysis was the improvement in Fleet readiness. Integrated production of technical manuals and training courses would increase the likelihood of providing the Fleet with up-to-date and consistent information, thus providing some insurance to the Navy's policy of fielding new systems and equipment upgrades only when the appropriate logistics support is available. A parametric analysis indicates that increasing the availability of the electronic, ordnance and HM&E components of a single new DDG 1000 destroyer by a single month would yield a gain in effectiveness the Navy values at \$2 million.



2003 - 2010 Sponsored Research Topics

Acquisition Management

- Acquiring Combat Capability via Public-Private Partnerships (PPPs)
- BCA: Contractor vs. Organic Growth
- Defense Industry Consolidation
- EU-US Defense Industrial Relationships
- Knowledge Value Added (KVA) + Real Options (RO) Applied to Shipyard Planning Processes
- Managing the Services Supply Chain
- MOSA Contracting Implications
- Portfolio Optimization via KVA + RO
- Private Military Sector
- Software Requirements for OA
- Spiral Development
- Strategy for Defense Acquisition Research
- The Software, Hardware Asset Reuse Enterprise (SHARE) repository

Contract Management

- Commodity Sourcing Strategies
- Contracting Government Procurement Functions
- Contractors in 21st-century Combat Zone
- Joint Contingency Contracting
- Model for Optimizing Contingency Contracting, Planning and Execution
- Navy Contract Writing Guide
- Past Performance in Source Selection
- Strategic Contingency Contracting
- Transforming DoD Contract Closeout
- USAF Energy Savings Performance Contracts
- USAF IT Commodity Council
- USMC Contingency Contracting

Financial Management

- Acquisitions via Leasing: MPS case
- Budget Scoring
- Budgeting for Capabilities-based Planning



- Capital Budgeting for the DoD
- Energy Saving Contracts/DoD Mobile Assets
- Financing DoD Budget via PPPs
- Lessons from Private Sector Capital Budgeting for DoD Acquisition Budgeting Reform
- PPPs and Government Financing
- ROI of Information Warfare Systems
- Special Termination Liability in MDAPs
- Strategic Sourcing
- Transaction Cost Economics (TCE) to Improve Cost Estimates

Human Resources

- Indefinite Reenlistment
- Individual Augmentation
- Learning Management Systems
- Moral Conduct Waivers and First-tem Attrition
- Retention
- The Navy's Selective Reenlistment Bonus (SRB) Management System
- Tuition Assistance

Logistics Management

- Analysis of LAV Depot Maintenance
- Army LOG MOD
- ASDS Product Support Analysis
- Cold-chain Logistics
- Contractors Supporting Military Operations
- Diffusion/Variability on Vendor Performance Evaluation
- Evolutionary Acquisition
- Lean Six Sigma to Reduce Costs and Improve Readiness
- Naval Aviation Maintenance and Process Improvement (2)
- Optimizing CIWS Lifecycle Support (LCS)
- Outsourcing the Pearl Harbor MK-48 Intermediate Maintenance Activity
- Pallet Management System
- PBL (4)
- Privatization-NOSL/NAWCI
- RFID (6)



- Risk Analysis for Performance-based Logistics
- R-TOC AEGIS Microwave Power Tubes
- Sense-and-Respond Logistics Network
- Strategic Sourcing

Program Management

- Building Collaborative Capacity
- Business Process Reengineering (BPR) for LCS Mission Module Acquisition
- Collaborative IT Tools Leveraging Competence
- Contractor vs. Organic Support
- Knowledge, Responsibilities and Decision Rights in MDAPs
- KVA Applied to AEGIS and SSDS
- Managing the Service Supply Chain
- Measuring Uncertainty in Earned Value
- Organizational Modeling and Simulation
- Public-Private Partnership
- Terminating Your Own Program
- Utilizing Collaborative and Three-dimensional Imaging Technology

A complete listing and electronic copies of published research are available on our website:
www.acquisitionresearch.org



THIS PAGE INTENTIONALLY LEFT BLANK





ACQUISITION RESEARCH PROGRAM
GRADUATE SCHOOL OF BUSINESS & PUBLIC POLICY
NAVAL POSTGRADUATE SCHOOL
555 DYER ROAD, INGERSOLL HALL
MONTEREY, CALIFORNIA 93943

www.acquisitionresearch.org



Institute for Defense Analyses

4850 Mark Center Drive • Alexandria, Virginia 22311-1882

***Cost-Benefit Study of a Project to Lower Cost and
Improve Readiness Through Integrating the
Management of Technical Information***

Dan Levine

May 2010

Cleared for Public Release

- Current problems with managing data for Navy technical manuals and training courses
- “Bridge” project to relieve these problems by integrating (“Bridging”) the production of technical manuals and training courses
- IDA cost-benefit analysis of the Bridge
- Methodology for estimating the benefits
- Quantitative results
- Sensitivity analysis
- Further work



Current Problems with Managing Data for Technical Manuals and Training Courses

- Content management processes are non-integrated
- Tech writers and course developers obtain OEM contractor data in parallel
- Data are stored in different formats
- Data are stored in different repositories
- Course developers use different tools
- No systematic way to identify data requiring modification by equipment upgrades via ECPs (Engineering Change Proposals)



Bridge Project to Relieve Problems

- Proposal to integrate (“Bridge”) the management of data for technical manuals and training courses
 - Project is funded by OSD(AT&L)
 - Part of OSD RTOC program (Reduction of Total Ownership Costs)
- What are the expected costs and benefits of integration?
 - Are the benefits substantial?
 - Do they cover the costs?

	Production of Technical Manuals and Training Courses	
	Current Processes	Bridge
Content management	Non-integrated	Integrated
OEM data	Obtained in parallel	Obtained once
Data format	Various	Common—S1000D industry specification
Data repository	Various	Common—CSDBs
Course developer authoring tools	Various	Various, but with common link (API) to CSDBs
Identification of data requiring modification by ECPs	No systematic method	Single tool (Web Service)



Cost Benefit Analysis of the Bridge

- **Costs**
 - Investment
 - personnel cost of project
 - Implementation
 - training future tech writers and course developers to use the Bridge
 - Change in site licenses and user fees to maintain CSDBs
- **Benefits**
 - Reduction in future cost of technical manuals and training courses
 - Improvement in shipboard readiness through timely delivery of information (parametric analysis)
- **Calculate 10-year costs and benefits (present values) using 2.4% annual discount rate mandated by OMB**

- Analyze a nominal 500-page technical manual and nominal one-content-hour training course
 - Identify the detailed tasks
 - Estimate the staff hours to perform these tasks using current processes and the Bridge
 - Calculate Bridge savings (5.3% and 15.3% for manuals and courses)
 - Use pay rates to convert staff hour savings to cost savings
- Scale up the savings to two samples of Navy manuals and courses



Two Samples for Analysis of Savings

- OSD perspective
 - Reduction in total ownership costs
 - Would the benefits cover the costs for all Navy (and DoD) manuals and courses?
 - Apply Bridge to a large sample: all HM&E (Hull, Mechanical and Electrical) manuals and all NeL (Navy e-Learning) delivered courses
- LCS Program Office perspective
 - Would integration save money for a single system?
 - Apply Bridge to LCS mine hunting sonar (AN/AQS-20A)



Examples of Staff-Hour Changes Using the Bridge

	Staff Hours
Increase in cost	
Draft new business rules to integrate technical data and training	60
Coordinate technical data with training activities	44
Reduction in cost	
Greater data reuse	160
Web Service to modify technical information in response to ECPs	280
Use Web Service to update links with training product	72
Develop storyboards for training courses	16
Publish content in Learning Management Systems	11



Quantitative Analysis: Base Case


	10-Year Benefits (Present Value)
OSD Perspective (HM&E/NeL)	
Costs (investment, implementation)	\$8.7 million
Benefits (future savings)	\$86.8 million
Net benefit (benefits less costs)	\$78.1 million
LCS Perspective (mine hunting sonar)	
Benefits	\$305.7 thousand

- Study uses historical data
 - Production of HM&E technical manuals (NAVSSSES)
 - Annual content hours of Navy e-Learning training courses (NETC)
 - Manuals and Courses for mine-hunting sonar (NTSP)
- But the savings also depend on uncertain inputs

	Net Benefits	
	Base Case	Variation
Variations that lower net benefits		
100% higher investment cost	\$1.8 million	\$ 3.6 million
200% higher implementation cost	\$6.9 million	\$ 20.7 million
50% lower training course cost savings	15.3%	7.65%
Variations that raise net benefits		
50% higher hourly pay rate	\$65	\$97
50% higher hard skills rate	50%	75%



Results of Sensitivity Analysis (Net Benefits)

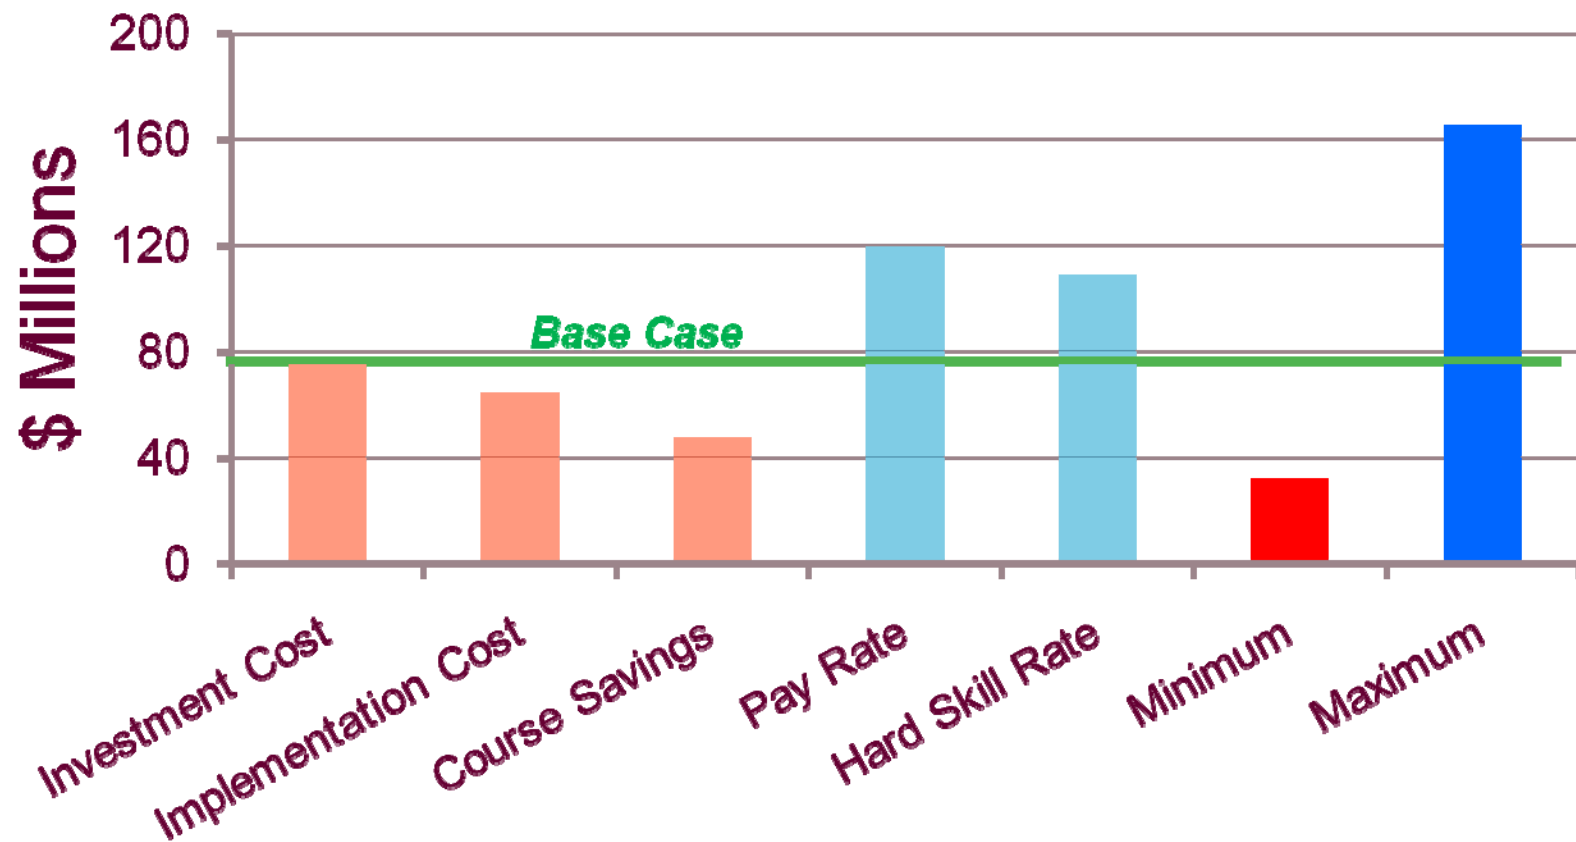

Applying the Bridge to all Navy (& DoD) manuals and courses
would increase net benefits

- Validate inputs during 2nd year of study

BACKUPS



Results of Sensitivity Analysis: OSD Perspective

	10-Year Net Benefits (Present Values)
Variations that lower net benefits	
100% higher investment costs	\$76 million
200% higher implementation costs	\$64 million
7.65% training course savings (vice 15.3%)	\$48 million
Variations that raise net benefits	
50% higher pay rate	\$120 million
75% hard skills (vice 50%)	\$109 million
Base Case	\$78 million
Minimum (all variations that lower net benefit)	\$32 million
All changes	\$77 million
Maximum (all higher net benefit)	\$166 million

Increasing sample to all Navy (DoD?) manuals and courses
would increase net benefits

- Recent Navy policy: after shipyard availabilities, don't deploy ships with new systems and equipment upgrades until all logistics support is in place
- Effect of the Bridge
 - Earlier completion of logistics support (manuals and courses)
 - Allow ships to be deployed sooner
- Parametric analysis: Permitting a single DDG-1000 to deploy a single month earlier would increase effectiveness of electronic, ordnance and HM&E components the Navy values as \$2 million.
