



**Carnegie Mellon
Software Engineering Institute**

Pittsburgh, PA 15213-3890

Defining Acquisition Measures The Integrated Software Acquisition Measurement Project (ISAM)

Software Engineering Institute
Carnegie Mellon University
Pittsburgh, PA 15213-3890

Dr. John Mishler, NAVAIR Resident Affiliate, SEI, 2002-2003

Mr. Frank Sisti, Senior Member of the Technical Staff, SEI

**Sponsored by the U.S. Department of Defense
© 2002 by Carnegie Mellon University**

Report Documentation Page				Form Approved OMB No. 0704-0188	
Public reporting burden for the collection of information is estimated to average 1 hour per response, including the time for reviewing instructions, searching existing data sources, gathering and maintaining the data needed, and completing and reviewing the collection of information. Send comments regarding this burden estimate or any other aspect of this collection of information, including suggestions for reducing this burden, to Washington Headquarters Services, Directorate for Information Operations and Reports, 1215 Jefferson Davis Highway, Suite 1204, Arlington VA 22202-4302. Respondents should be aware that notwithstanding any other provision of law, no person shall be subject to a penalty for failing to comply with a collection of information if it does not display a currently valid OMB control number.					
1. REPORT DATE JAN 2003		2. REPORT TYPE		3. DATES COVERED 00-00-2003 to 00-00-2003	
4. TITLE AND SUBTITLE Defining Acquisition Measures The Integrated Software Acquisition Measurement Project (ISAM)				5a. CONTRACT NUMBER	
				5b. GRANT NUMBER	
				5c. PROGRAM ELEMENT NUMBER	
6. AUTHOR(S)				5d. PROJECT NUMBER	
				5e. TASK NUMBER	
				5f. WORK UNIT NUMBER	
7. PERFORMING ORGANIZATION NAME(S) AND ADDRESS(ES) Carnegie Mellon University,Software Engineering Institute,Pittsburgh,PA,15213				8. PERFORMING ORGANIZATION REPORT NUMBER	
9. SPONSORING/MONITORING AGENCY NAME(S) AND ADDRESS(ES)				10. SPONSOR/MONITOR'S ACRONYM(S)	
				11. SPONSOR/MONITOR'S REPORT NUMBER(S)	
12. DISTRIBUTION/AVAILABILITY STATEMENT Approved for public release; distribution unlimited					
13. SUPPLEMENTARY NOTES					
14. ABSTRACT					
15. SUBJECT TERMS					
16. SECURITY CLASSIFICATION OF:			17. LIMITATION OF ABSTRACT Same as Report (SAR)	18. NUMBER OF PAGES 27	19a. NAME OF RESPONSIBLE PERSON
a. REPORT unclassified	b. ABSTRACT unclassified	c. THIS PAGE unclassified			



**Carnegie Mellon
Software Engineering Institute**

Software Engineering Institute

DoD R&D Laboratory FFRDC

Sponsored by OUSD (AT&L)

Created in 1984

**Under contract to
Carnegie Mellon University**

**Offices in Arlington VA and
Pittsburgh PA**

**Mission: Improve the
practice of software
engineering**





JAC Challenge Problem for the SEI

The SEI Joint Advisory Committee (JAC)

- Is a tri-service oversight board to guide the SEI.
- Establishes SEI goals and direction.

One key challenge the JAC gave to the SEI is to define acquisition measurements to

- measure and manage software-intensive systems
- promptly, accurately, and precisely describe project status and trends
- support DoD program managers



SEI's Acquisition Support Program

The SEI has established the Acquisition Support Program (ASP) to address system acquisition issues.

The Integrated Software Acquisition Measurement (ISAM) project is SEI's first step in addressing the acquisition measurement challenge.

The full Team Acquisition Process (TAP) effort will be a follow-on ASP project to address broader acquisition management needs.



Acquisition Measurement Objectives

The ISAM project aims to develop integrated measures that

- apply to all development and acquisition levels
- provide broad life-cycle coverage
- promptly and precisely portray program status
- accurately predict future program performance
- minimally intrude on the development work
- support cyclic development
- facilitate process improvement
- are a natural consequence of quality work

The goal is to build a measurement culture at all levels of development and acquisition organizations.



Metrics Program Requirements

To obtain useful measures, work must be precisely planned – without precise plans, work cannot be precisely tracked.

The development process must also be defined – undefined processes cannot be measured.

Process and product quality must be measured and managed – poor quality work makes projects late and unpredictable.

A useful metrics program must have people who consistently gather accurate data and know how to use these data.



The SEI Team Software Process

Software-intensive programs will not improve until the behavior of the software professionals changes.

The SEI has developed and is now transitioning the Team Software Process (TSP)SM into general practice.

With the TSP, precise measures are a basic and normal part of engineering practice.

The TSP provides the management and engineering training needed for rapid deployment and effective use of measures.

TSP projects predictably deliver the safe, secure, and high-quality software-intensive systems needed for modern warfare.

SM

Team Software Process and TSP are service marks of Carnegie Mellon University.



The TSP Is Widely Used

Some of the organizations that are introducing and using the TSP are

ABB

AIS

Bechtel

Boeing

Comnet

DFAS

EDS

Ericsson

Honeywell

lomega

Kaiser

Litton

Microsoft

NASA Langley

SAIC

SDRC

Teradyne

USAF: Hill AFB

USN: NAVAIR

USN: NAVOCEANO

USN: NUWC

Xerox



TSP Measurements

With the TSP, developers measure all of their work.

- time spent by phase
- size of products produced
- defects found by phase and product element

From these data, all required engineering project management measures can be derived.


When using the TSP, development teams know precisely where their projects stand.

TSP teams regularly report on plan versus actual quality and schedule status, estimated project completion, and status of significant risks.



Predictable Schedules

**Schedule Deviation Individual Value Control Chart -
Commercial Systems**

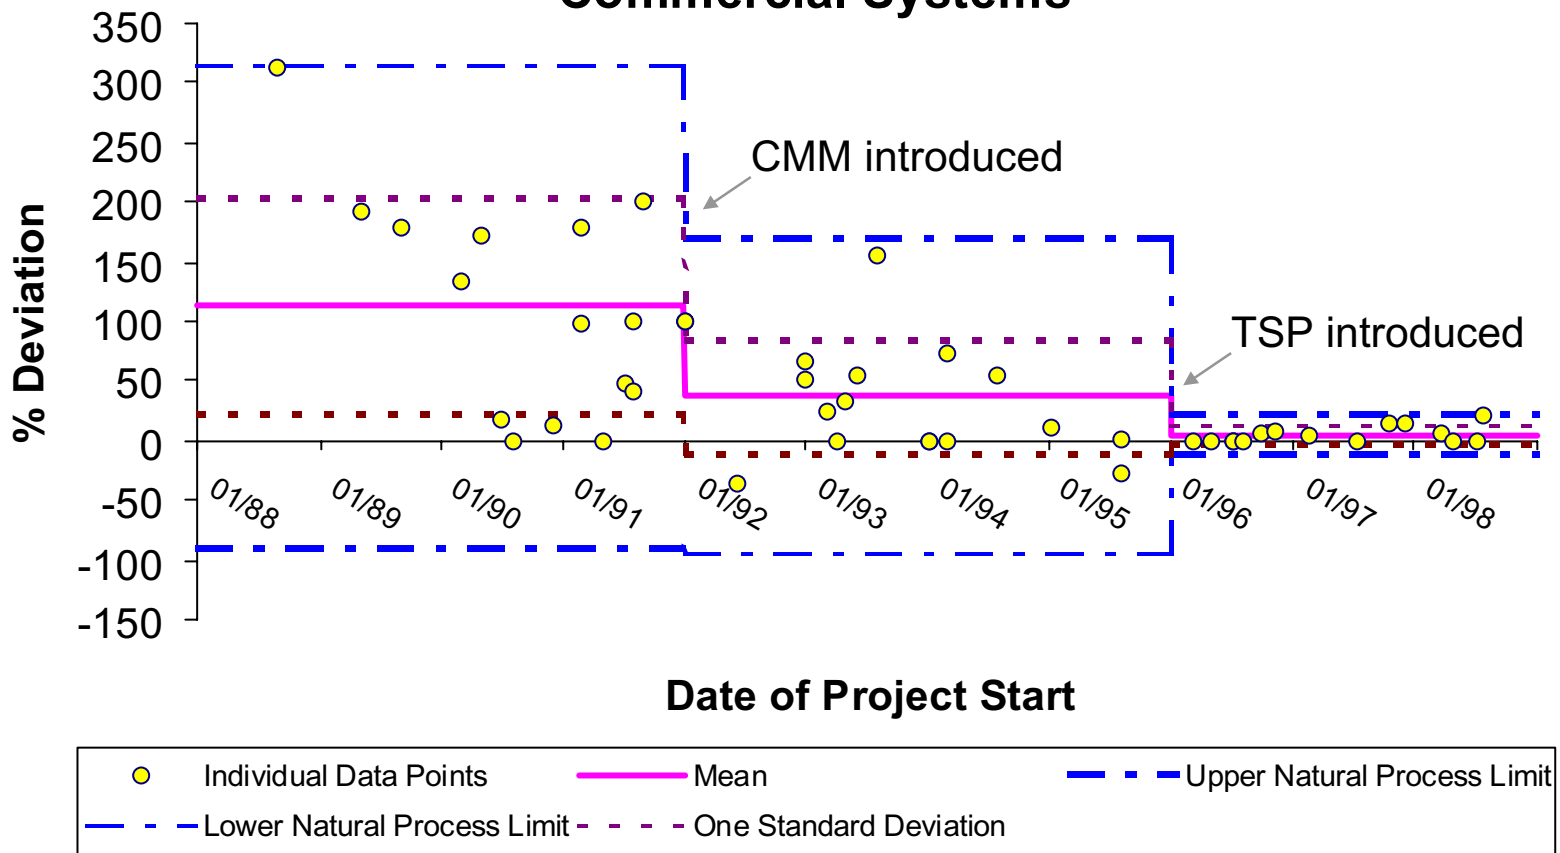


[Source: AIS]



Cost and Schedule Performance

Sound budgets and commitments require accurate size and resource estimates.

Data from 24 teams in 4 organizations show that TSP teams make accurate estimates.

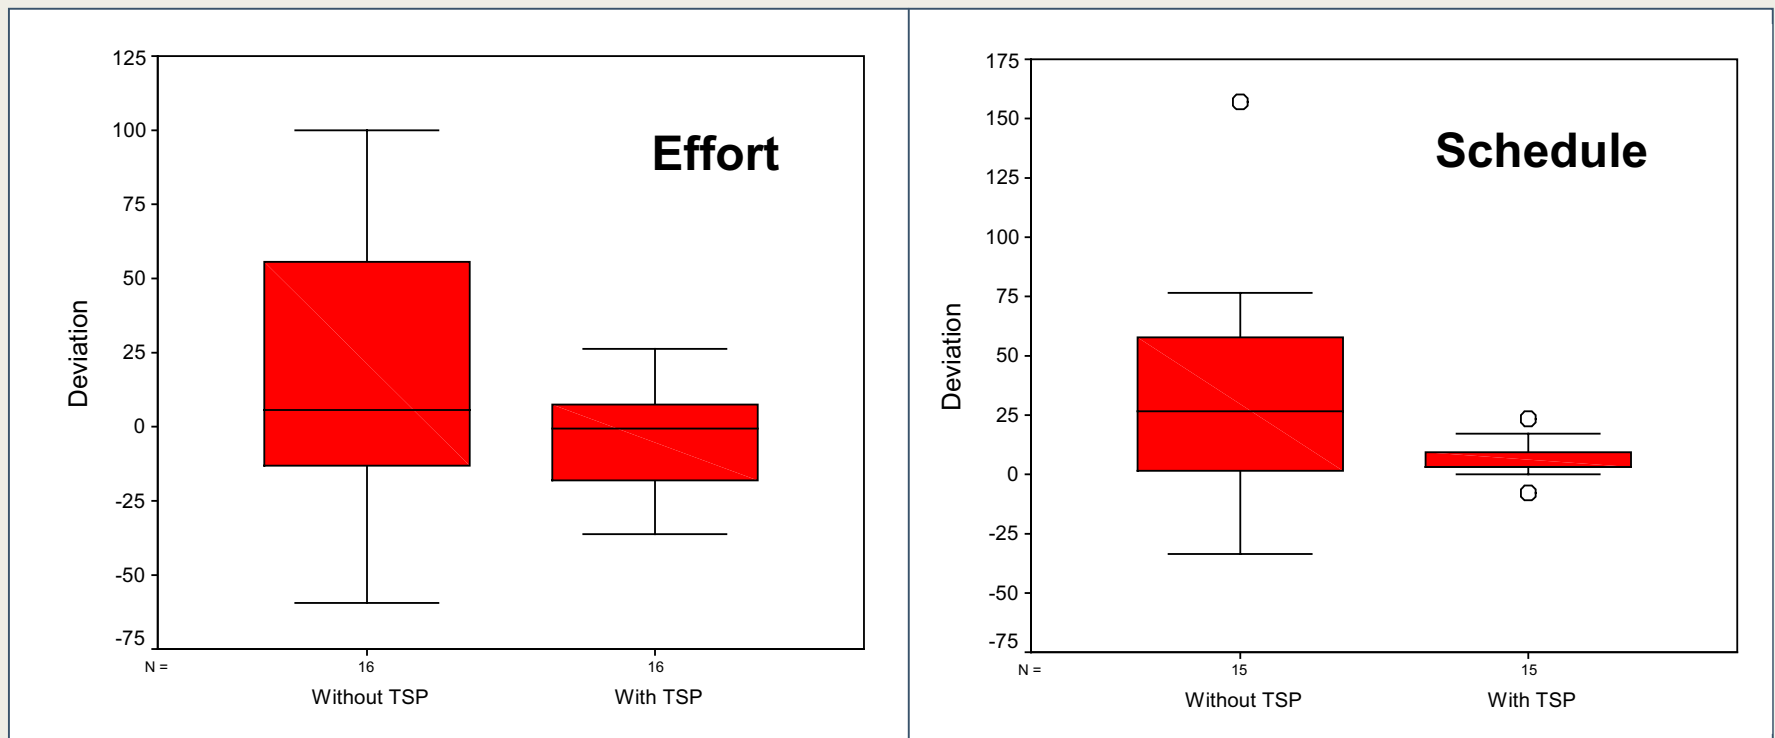



TSP Quality Management


With the TSP, teams consistently improve product quality.

By doing quality work, TSP teams

- accelerate development schedules
- reduce program costs
- sharply cut testing time
- greatly reduce maintenance effort




TSP Quality Benefits - Boeing

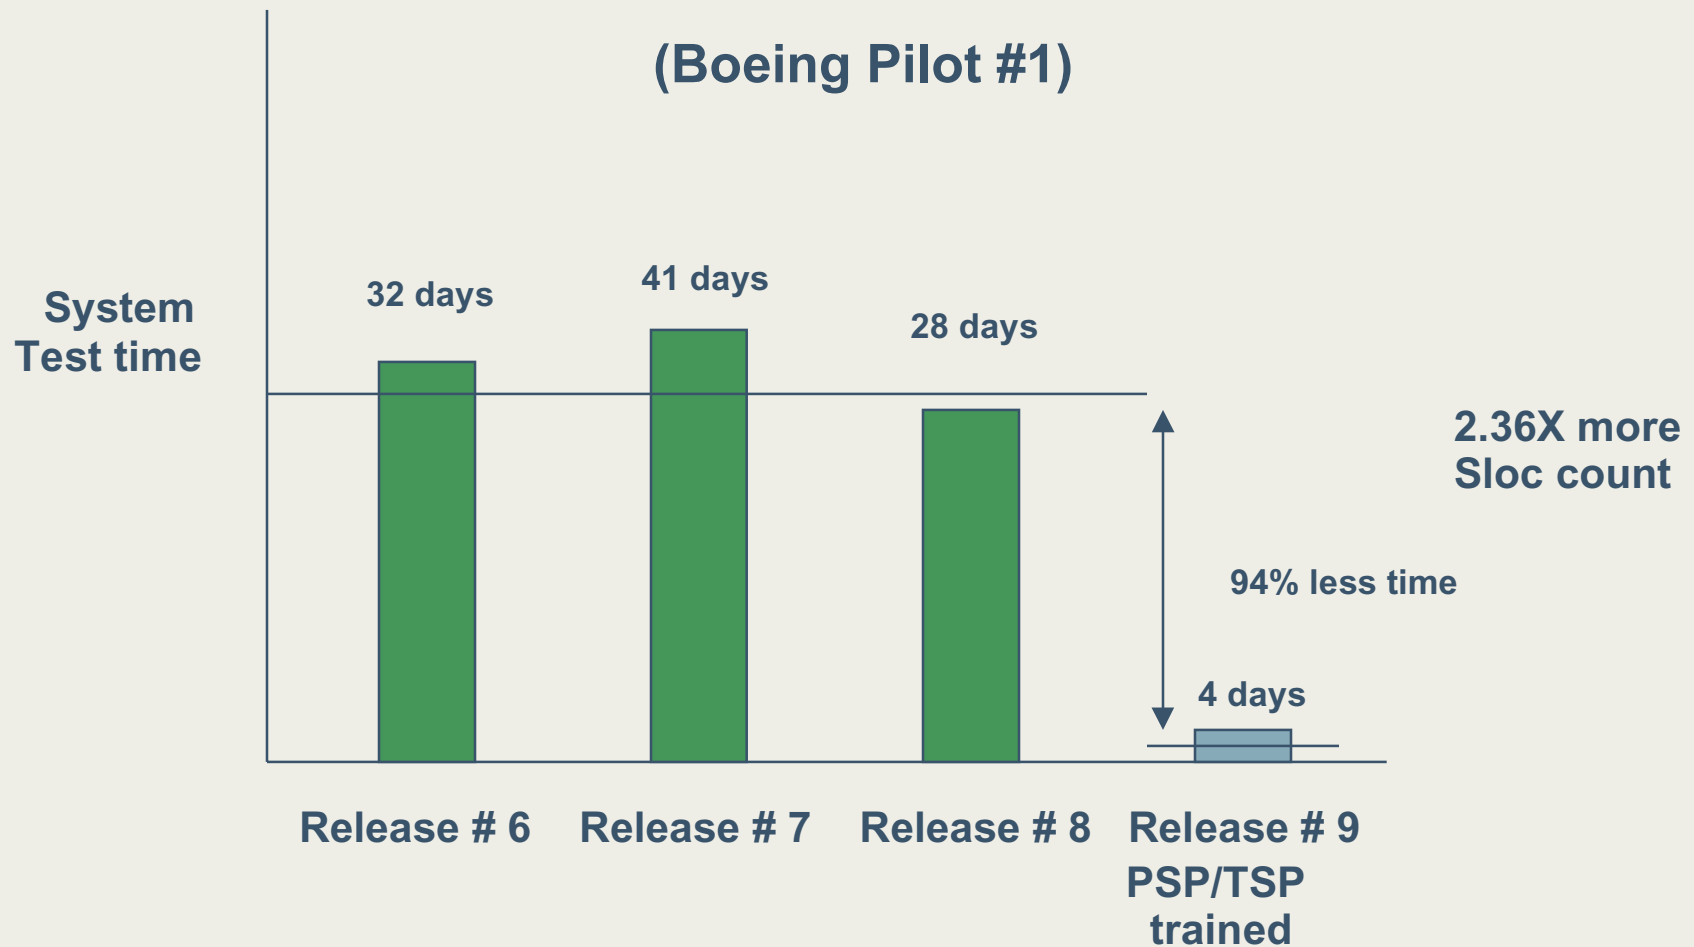




Higher Product Quality

By planning, measuring, and tracking quality, TSP projects have fewer defects and shorter testing times.

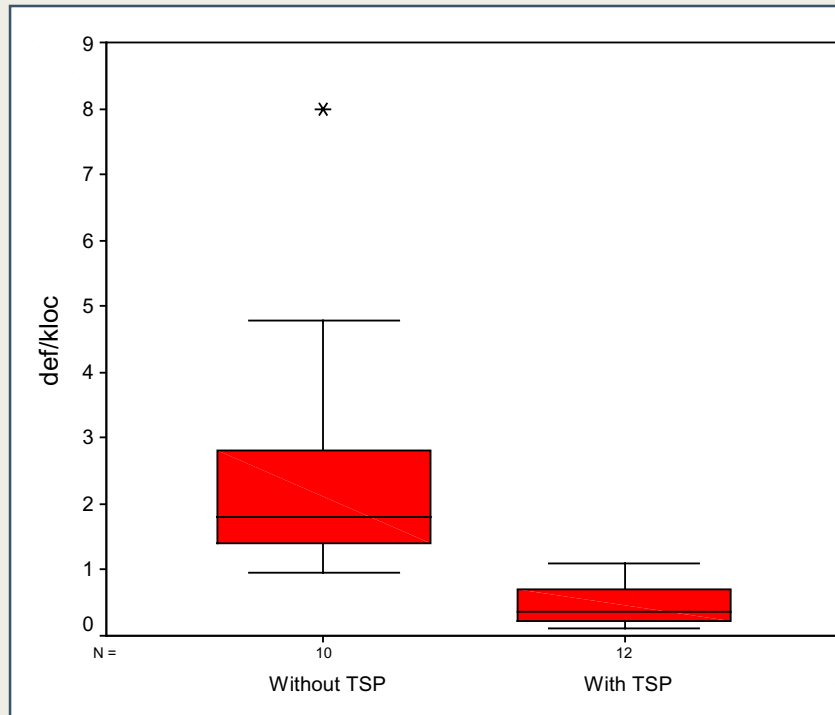

System test defect density

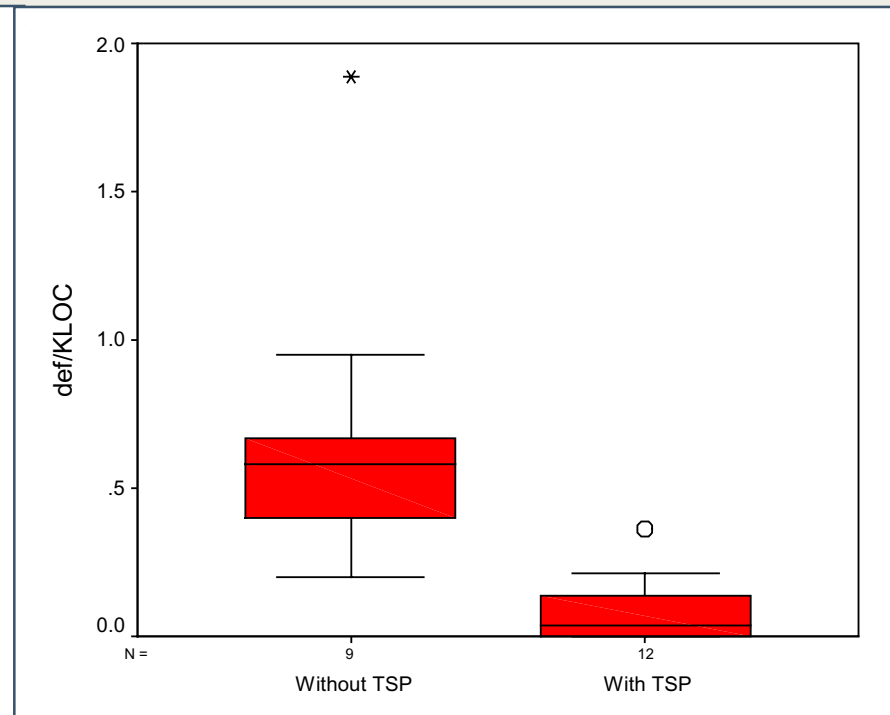

Acceptance test defect density



Reduced Cycle Time

Typical team

Reqts	Design	Implement	Test
-------	--------	-----------	------

TSP team


Reqts	Design	Implement	Test
-------	--------	-----------	------

Savings

With the TSP, teams find and fix defects early in the development process.

This sharply reduces test time.


With shorter testing, cycle time is cut.

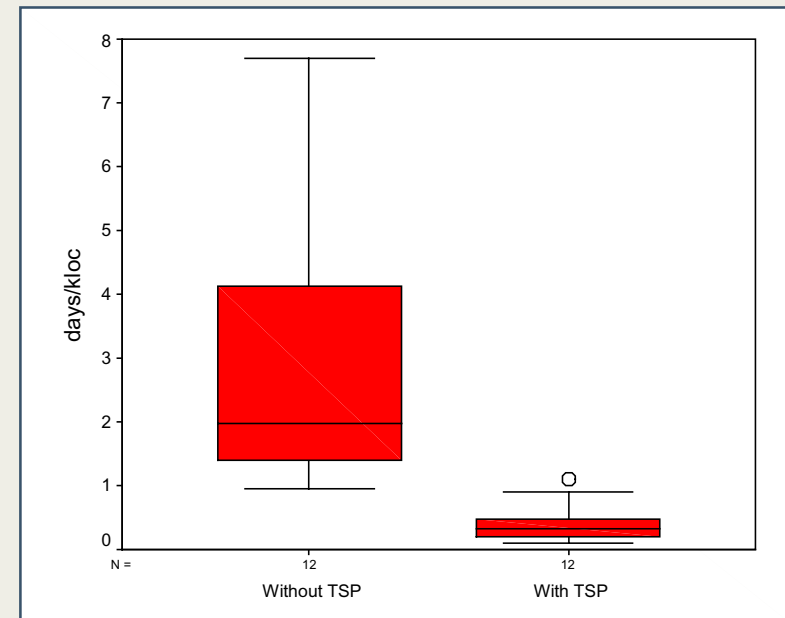

Test Time per KLOC



Reduced Development Costs

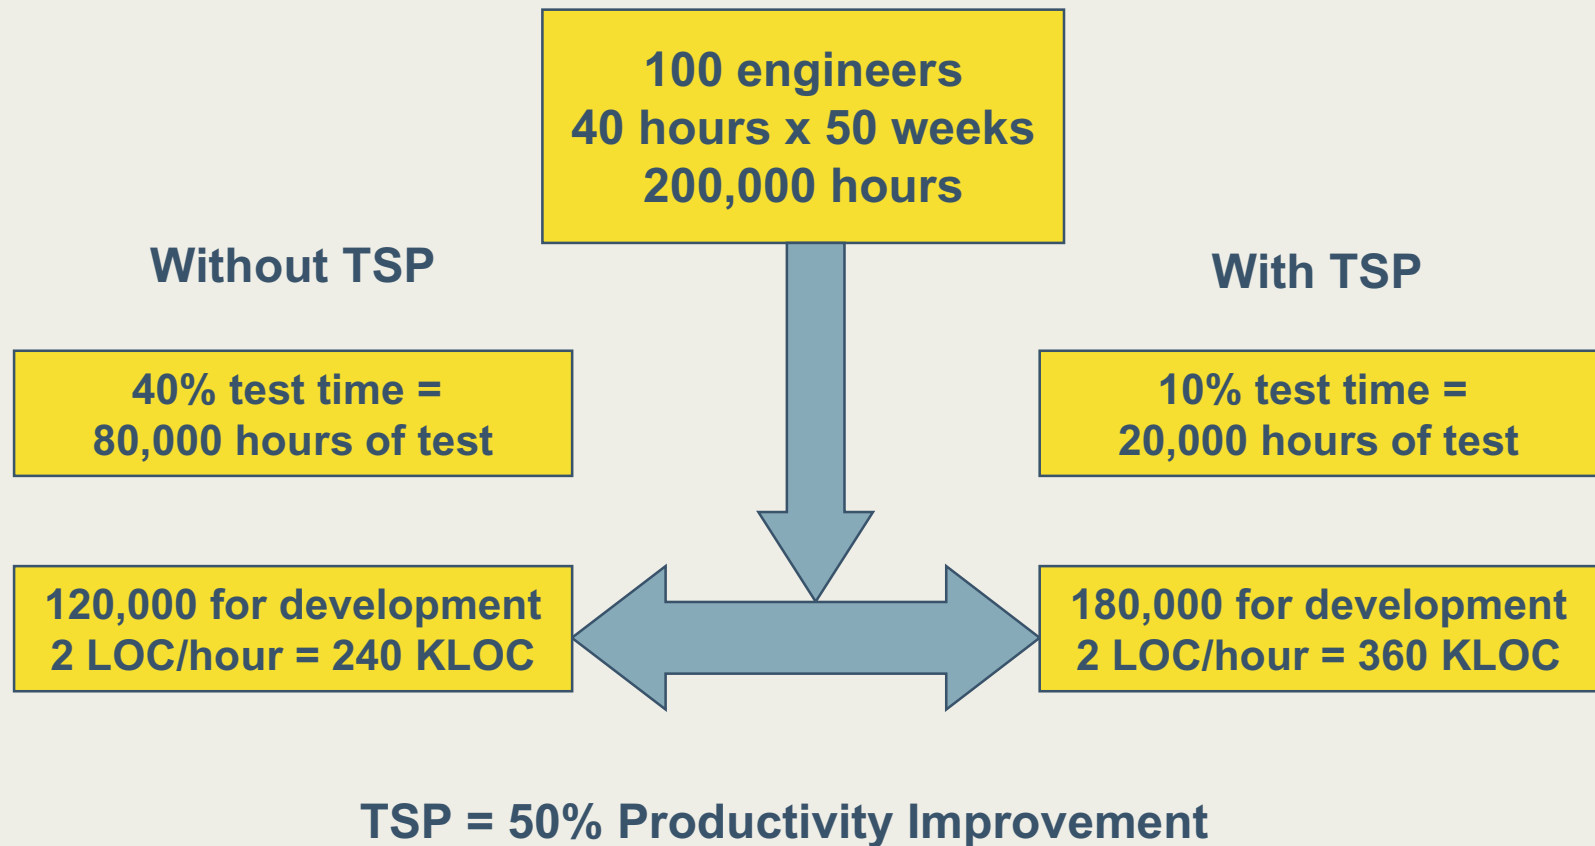



The ISAM Measurement Focus

Product



Product Focus

- Customer Satisfaction (CUPRIMDSPS)
- Operational Capability
- Initial Operational Capability (IOC) Support
- Integrated Logistics Support (ILS) Plan
- System Integration (System of Systems)

Other Focus

- Legal
- Financial
- Contracts
- Customer
- Sponsor

Project Focus – ISAM

- Schedule (projection, status, trend)
- Cost (projection, status, trend)
- Defects (projection, status, trend)
- Project Cycle Time
- Total Ownership Cost (TOC)
- Cost of Quality
- Requirements Satisfaction

Process Focus

- Cycle time trends
- Support Capability
- Total Ownership Cost trends
- Requirements Management





Effective Program Measurement

To be useful for management, measures must be

- precisely defined, accurate, and traceable
- timely and predictive
- used by engineering
- a minimum complete and consistent set

The TSP accomplishes this by providing comprehensive measurements that are integral to the engineering work.

With TSP, measurement is natural. The TSP



- precisely and promptly measures the engineering work
- does not impose added measurement costs
- provides a defined and non-proprietary measurement system



Schedule Predictability

The schedule predictability measures are

- earned value
- completion projections
- completion projection trends

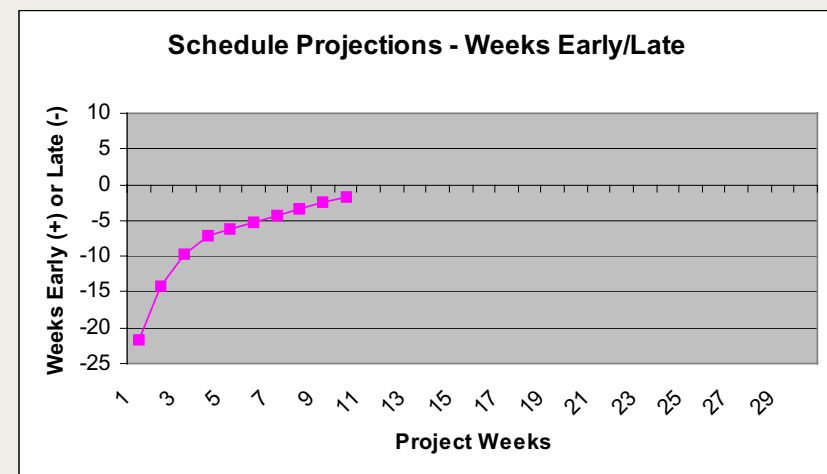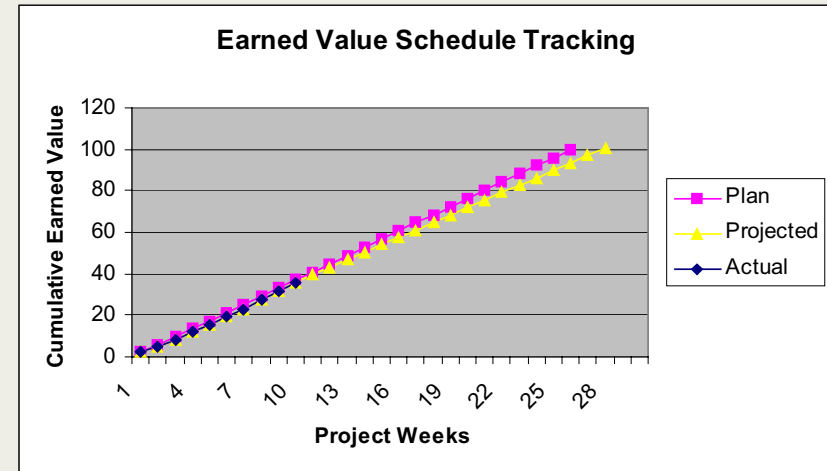





Effort Predictability

Actual versus planned task hours

Billed hours versus task hours

Relationship of task hours and EV status

Effort estimate accuracy for completed tasks

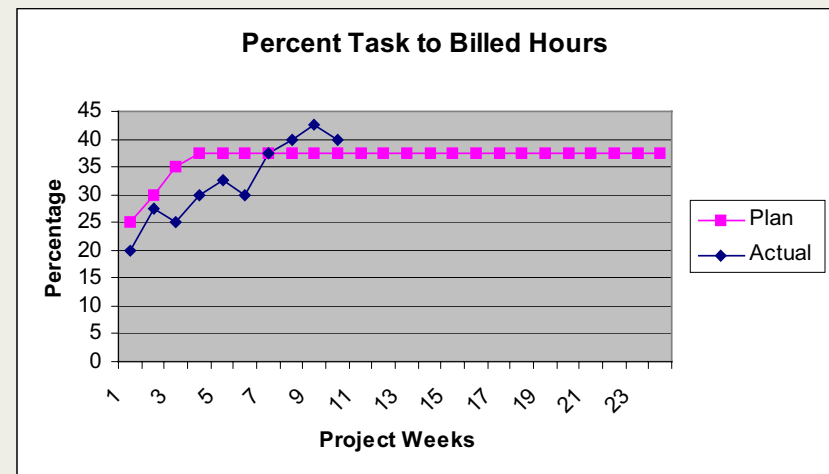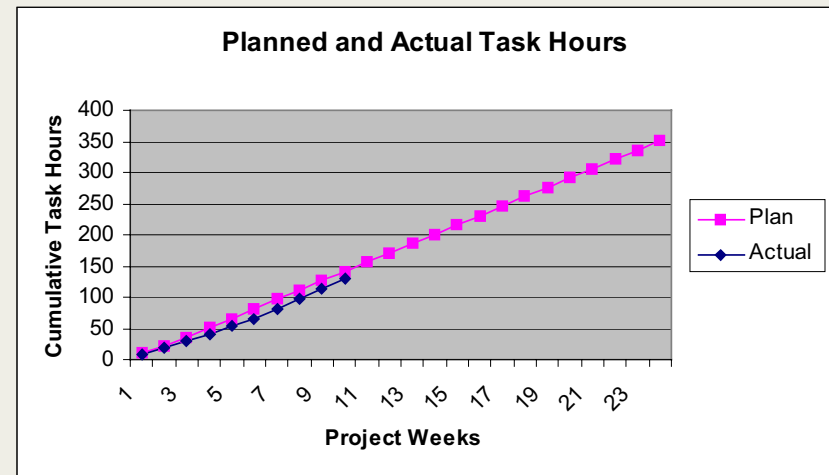





Quality

Defects per KLOC,
planned and actual

Percent defect free (PDF)

Quality profiles

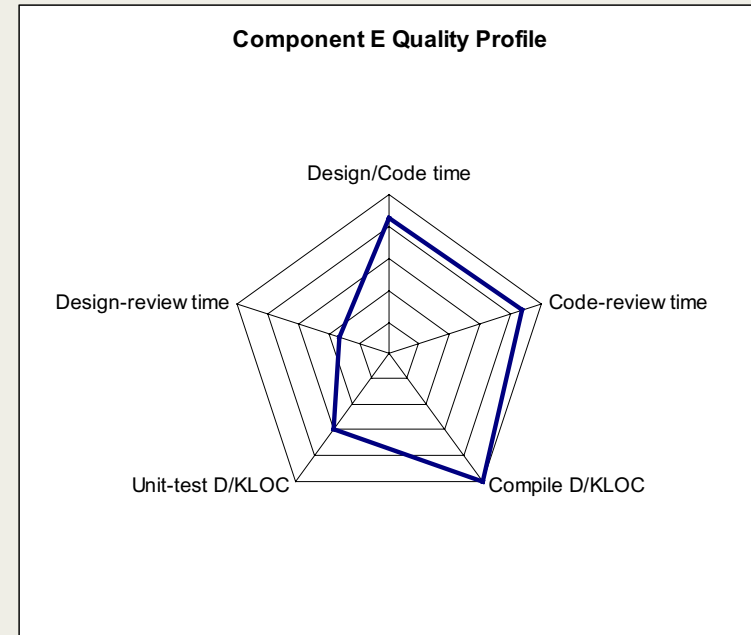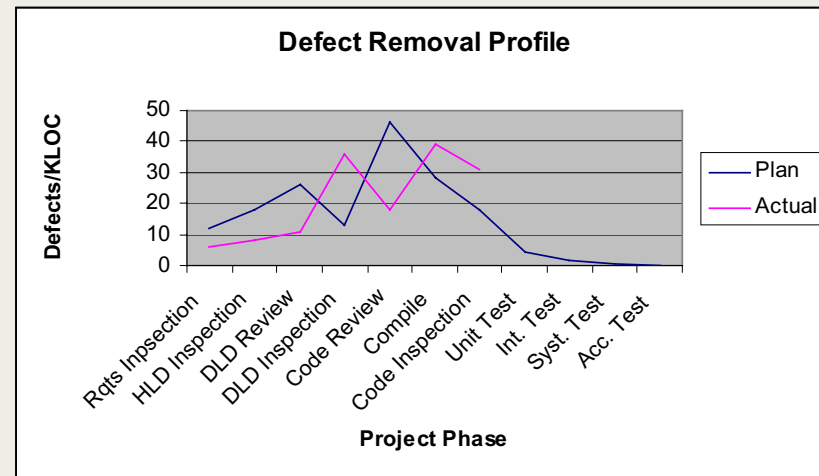




Cycle Time Reduction

Time in days from project initiation to initial operational capability

Time to first production article delivery

Percent of cycle time spent in test phases (after unit testing)

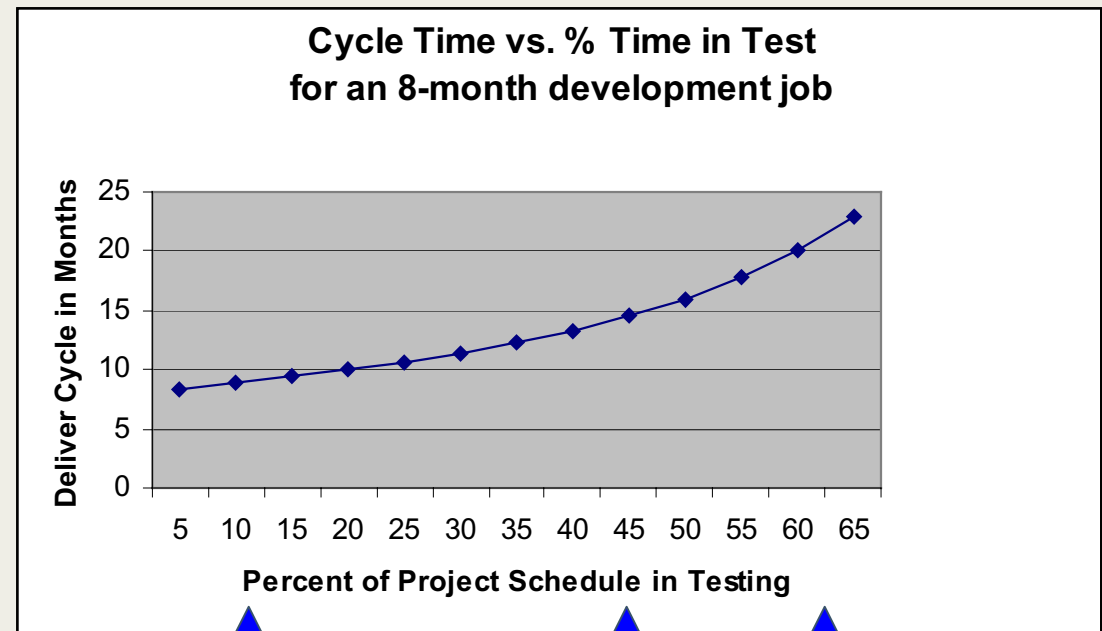

Typical
TSP
Projects

Typical
Projects

Large
System
Projects



Other Measures

Total Ownership Cost

- Cost of program development (program initiation to initial operational capability)
- Cost of program maintenance (cost to maintain product after initial operational capability)

Cost of Quality

- Percent of total development time spent in appraisal (walkthroughs, reviews, and inspections)
- Percent of total development time spent in rework (compile and test)

Requirements Satisfaction

- Number of acceptance test defects in user acceptance or operational suitability tests
- Acceptance test defects per KLOC



Required Training

To adopt these measures, acquisition groups will require a few days of ISAM training.

The development groups must use the TSP.

An extensive program is available for transitioning the TSP into development and maintenance organizations.

- Executive kickoff and planning seminar – 1 1/2 days
- Management training – 2 days
- Engineer training: 2 week PSP course
- Internal transition agent training
 - PSP Instructor – 5 days
 - TSP Launch Coach – 5 days

Training costs are recovered with the first 1,000 LOC developed.



Next Steps

Complete program management interviews.

Refine proposed measures.

Establish metrics-based management methods.

Define metrics prototype testing effort.

Conduct prototype tests

- Program managers use ISAM measurements.
- Projects use the TSP.

Produce final report and transition plan.



Conclusions

Improved measurements are needed to manage software-intensive systems throughout their life cycle.

The TSP provides the foundation for precise and timely program measurements.

ISAM provides the measurement tools for effective and responsive program management.

With your help and support, this project will guide future program managers in meeting our military's needs for reliable, safe, and secure software-intensive systems.



**Carnegie Mellon
Software Engineering Institute**

For Further Information

Please contact:

Anita D. Carlton
Senior Member of the Technical Staff
Software Engineering Institute
Carnegie Mellon University
Pittsburgh, PA 15213-3890

Tel. (412) 268-7718
