

SCAMPI-B for Contract Monitoring—A Case Study of the Mission Planning Enterprise Contractors

Sponsored by the U.S. Department of
Defense

Lorraine Adams, SEI
Kathy Bastien, BlueForce LLC
March 2007

SM SCAMPI is a service mark of Carnegie Mellon University

®CMMI and Capability Maturity Model are registered in the US Patent and Trade Office

© 2006 BlueForce LLC. All rights reserved



Software Engineering Institute

Carnegie Mellon

© 2006 Carnegie Mellon University

Report Documentation Page

*Form Approved
OMB No. 0704-0188*

Public reporting burden for the collection of information is estimated to average 1 hour per response, including the time for reviewing instructions, searching existing data sources, gathering and maintaining the data needed, and completing and reviewing the collection of information. Send comments regarding this burden estimate or any other aspect of this collection of information, including suggestions for reducing this burden, to Washington Headquarters Services, Directorate for Information Operations and Reports, 1215 Jefferson Davis Highway, Suite 1204, Arlington VA 22202-4302. Respondents should be aware that notwithstanding any other provision of law, no person shall be subject to a penalty for failing to comply with a collection of information if it does not display a currently valid OMB control number.

1. REPORT DATE MAR 2007	2. REPORT TYPE	3. DATES COVERED 00-00-2007 to 00-00-2007			
4. TITLE AND SUBTITLE SCAMPI-B for Contract Monitoring - A Case Study of the Mission Planning Enterprise Contractors		5a. CONTRACT NUMBER			
		5b. GRANT NUMBER			
		5c. PROGRAM ELEMENT NUMBER			
6. AUTHOR(S)		5d. PROJECT NUMBER			
		5e. TASK NUMBER			
		5f. WORK UNIT NUMBER			
7. PERFORMING ORGANIZATION NAME(S) AND ADDRESS(ES) Carnegie Mellon University ,Software Engineering Institute (SEI),Pittsburgh,PA,15213		8. PERFORMING ORGANIZATION REPORT NUMBER			
9. SPONSORING/MONITORING AGENCY NAME(S) AND ADDRESS(ES)		10. SPONSOR/MONITOR'S ACRONYM(S)			
		11. SPONSOR/MONITOR'S REPORT NUMBER(S)			
12. DISTRIBUTION/AVAILABILITY STATEMENT Approved for public release; distribution unlimited					
13. SUPPLEMENTARY NOTES					
14. ABSTRACT					
15. SUBJECT TERMS					
16. SECURITY CLASSIFICATION OF:			17. LIMITATION OF ABSTRACT	18. NUMBER OF PAGES	19a. NAME OF RESPONSIBLE PERSON
a. REPORT unclassified	b. ABSTRACT unclassified	c. THIS PAGE unclassified	Same as Report (SAR)	32	

Contents / Agenda

Background

What is SCAMPI-B for Contract Monitoring

SCAMPI-B for Contract Monitoring at MPEC

Program Office Changes Resulting from SCAMPI-B for Contract Monitoring

Lessons Learned

Way Ahead

Summary



DoD Weapon Systems Acquisition Still a High Risk Area

While DOD's acquisition process has produced the best weapons in the world, it also yields undesirable consequences in weapon system programs – cost increases, schedule delays, and performance shortfalls

Problems occur because weapon programs do not capture early on the requisite knowledge that is needed to effectively manage risks

Programs move forward with unrealistic cost and schedules estimates, lack clearly defined and stable requirements, use immature technologies, and fail to solidify design and manufacturing processes at appropriate junctures in development

As a result, programs require more resources than planned, the buying power of the defense dollar is reduced, and funds are not available for other competing needs

*Paul Francis, Director
Acquisition and Sourcing Management
U.S. Government Accountability Office
May 18, 2004*



Problem Statement

- A statement of organizational process maturity or capability level does not guarantee performance to that same level of proficiency on an individual project
- Most DoD contractors claim high maturity/capability levels, yet from the perspective of the acquirer, systems engineering and program management practices are severely lacking
- Teaming arrangements further cloud the issue of process execution and proficiency
- Associated problems may not be evident until significant cost, schedule, or performance objectives have been missed at a late point in the program where corrective actions are very costly

How can the acquirer gain the necessary insight into process execution and proficiency as well as reinforce desired behaviors?



The Mission Planning Solution and What was Learned

A “simple” solution - solve the problem through contract requirements

- All contractors must be at least CMM maturity level 3 to bid on IDIQ software development contracts
- All winning contractors must achieve CMMI maturity level 3 NLT 24 months after contract award

Monitor the contracts to assure that CMMI requirement is met by deadline

Conduct a round of CMMI baseline SCAMPI-Bs for Contract Monitoring to assist process improvement toward meeting that goal

The process of conducting 5 baseline SCAMPI-Bs for Contract Monitoring was an “eye opening” experience



What is SCAMPI-B for Contract Monitoring




High Maturity Organizations




High Maturity Projects

- Maturity Levels are indicators of organizational *potential performance*
- They describe how the next project may *perform* based on a sampling of existing projects
- Maturity Levels reside at the organizational level and are not an indication of how an individual project *is performing*

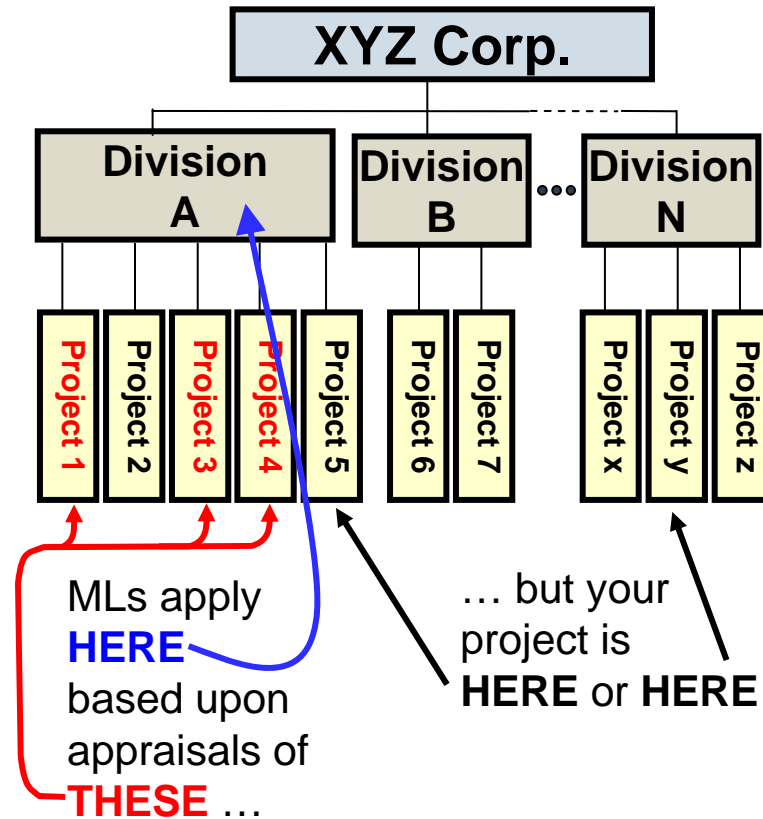

Standard CMMI Appraisal Method for Process Improvement (SCAMPI)

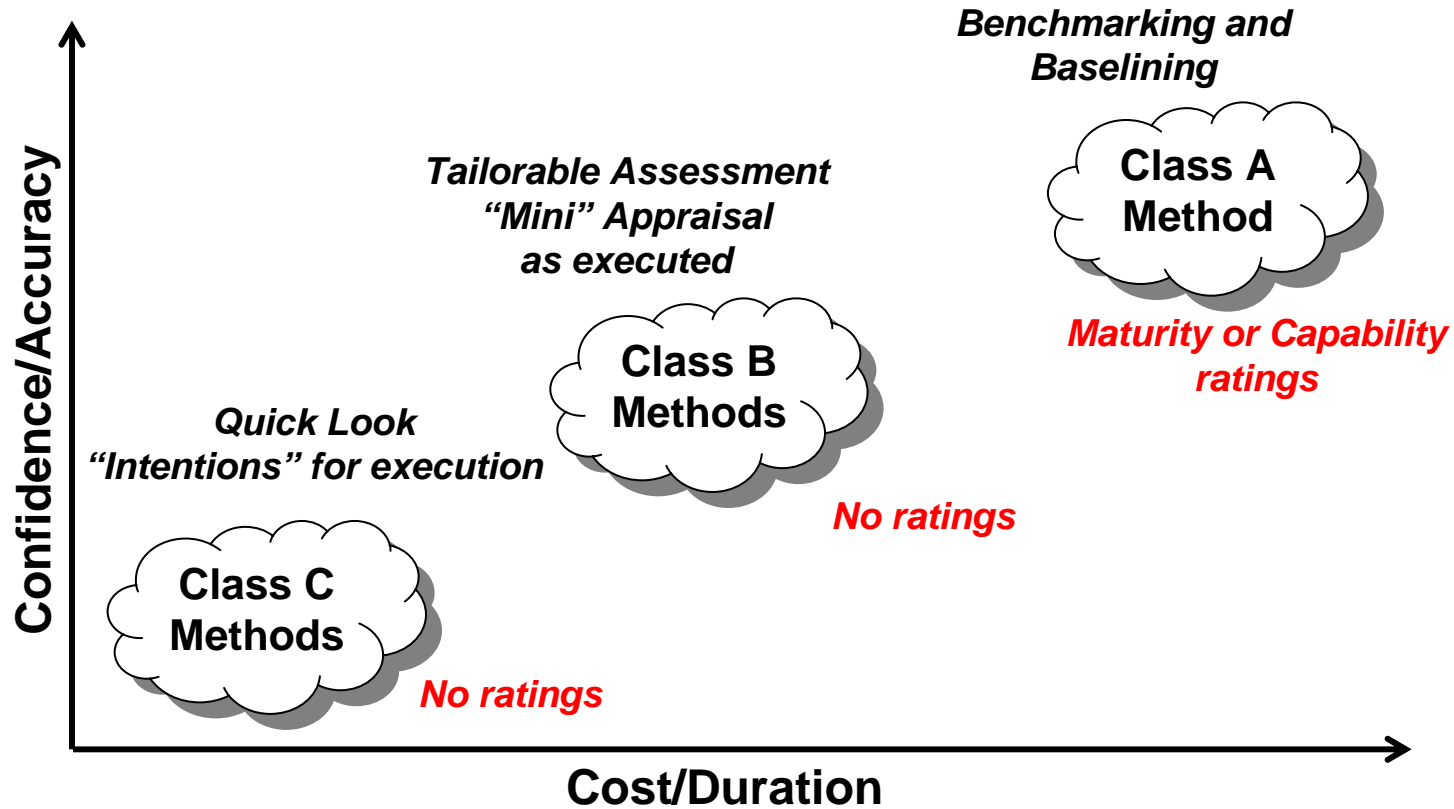

SCAMPI-B for Contract Monitoring Ground Rules - 1

Use the process model – CMMI

- Interview questions based on model

Appraisal of process performance and adherence

Focus on risk assessment – risks associated with process performance, adherence, and capability



SCAMPI-B for Contract Monitoring Ground Rules - 2

Observe strict confidentiality

- Results not attributable to individuals or interview groups

Approach SCAMPI collaboratively

Results in actionable findings by Program Office and/or Contractor




SCAMPI-B for Contract Monitoring for MPEC



Mission Planning Contracting Structure

Delivery Orders

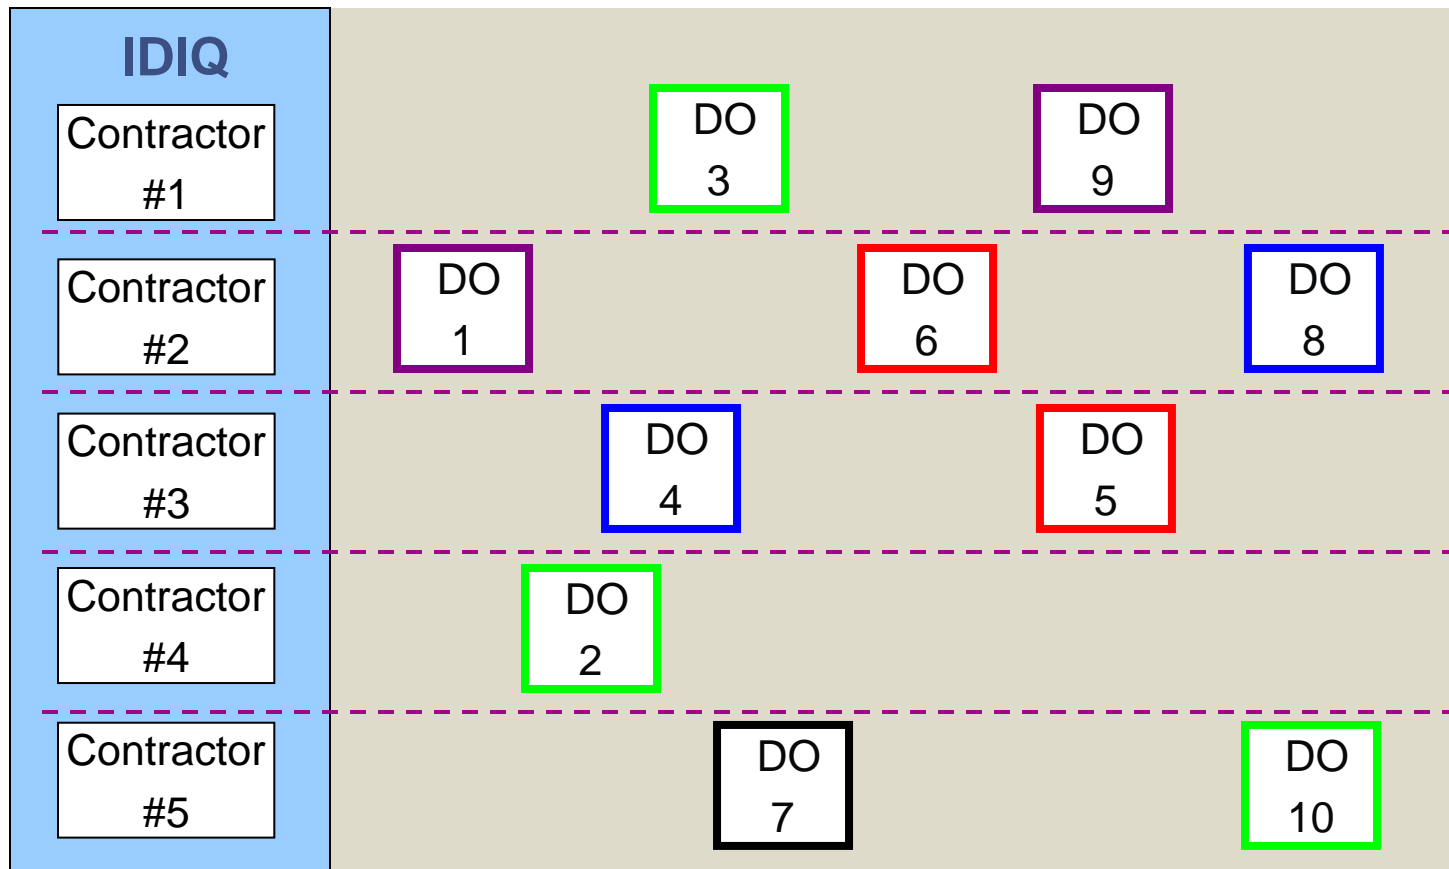

How SCAMPI-B for Contract Monitoring was Employed for MPEC - 1

Used appraisals to baseline compliance with CMMI requirement

- Demonstrate capability *or*
- Develop findings which yield improvement opportunities



One project would be selected from each contractor as a 'representative' of all Mission Planning projects for that contractor



How SCAMPI-B for Contract Monitoring was Employed for MPEC - 2

Appraisal findings would be used to assess progress toward meeting this the 24 month CMMI requirement

- Results to be factored into future DO competitions

Appraisal finding to be used for contract monitoring to identify areas of risk in project execution

Appraisal findings resulted in request for Process Improvement Plans from the contractors

- Way ahead to fix findings in representative project
- Way ahead to fix similar known deficiencies in all Mission Planning work



Program Office Changes Resulting from SCAMPI-B for Contract Monitoring



Results Changed the Way the Program Office Does Business - 1

- Contractor Process Improvement Plans and status are tied to contractor award fee
- RFP language has been modified to better reflect the program office desire for CMMI compliance across development teams – including subcontractors
- Based on input from appraisals, the program office is reviewing/modifying the standard CDRL list to get best ROI
- Business and technical rules for MP developers have been modified



Results Changed the Way the Program Office Does Business - 2



- Program Office is modifying internal processes to better take advantage of information provided through contractor's standard processes (e.g. metrics)

“In light of significant personnel cuts, we need to provide a smart way to provide a laser-like focus to our key issues. SCAMPI-B for Contract Monitoring reviews and EVM analysis provide that focus for us.”

*Steven A. Cote, GS-15, DAF
Deputy Director, 951st Electronic Systems Group*



Lessons Learned



Positive Lessons / Benefits - 1




Overcoming common misperceptions program offices have about CMMI

- What does a maturity level mean – *how is it attained*
- Need to *understand the scope* of previous appraisals and certifications
 - Organizational unit appraised



Positive Lessons / Benefits - 2

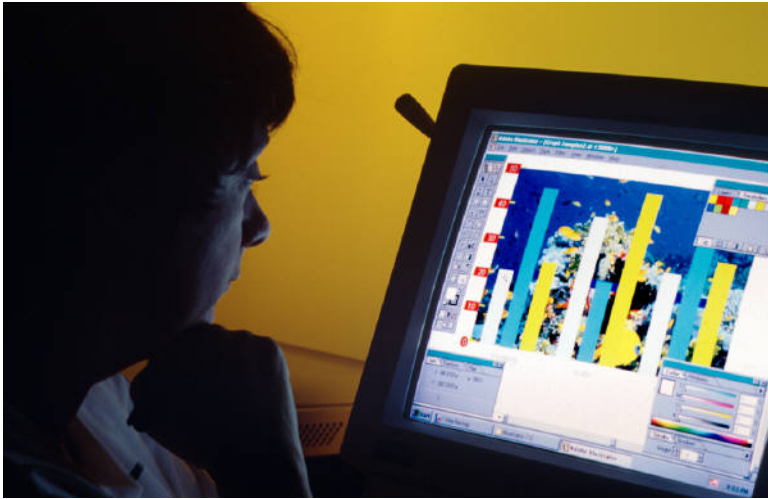

More savvy consumers

- **Monitoring** is more necessary than people think
- CMMI compliance and appraisal finding resolution should be tied into program office business activities
 - Award Fee Criteria (powerful motivator)
 - Business and Technical Rules
 - Proposal Evaluation Criteria



Positive Lessons / Benefits - 3

Appraisal results can be used to assist program management

- PMRs can *focus on areas of concern* based on findings

Uncovering program risks is more important than specific maturity levels



Real-time contract monitoring is key



Hard Lessons / Ongoing Challenges - 1



Spirit vs. letter of the model

- Assure *intent of the model* is met versus using “checklist” mentality
- Determine consistent approach to dealing with corporate “process lawyers”
- Shouldn’t judge “goodness,” but you should judge “*reasonableness*”



Hard Lessons / Ongoing Challenges - 2

Variability in the process itself, within the allowable scope of the method, can itself modify results

- Teams take on personalities based on membership (team members and lead appraisers)
- Different personalities can provide inconsistent results
- Need to ensure that decision criteria are ***consistently applied***
- Having a core group as a subset of each appraisal team provided a ***consistent methodology*** and ***interpretation of evidence***




Future Directions



Way Ahead -1

Mission Planning is reviewing options for verification of the November 2006 CMMI Maturity Level 3 requirement

- Accept results of contractor SCAMPI As?
 - Review of detailed appraisal results

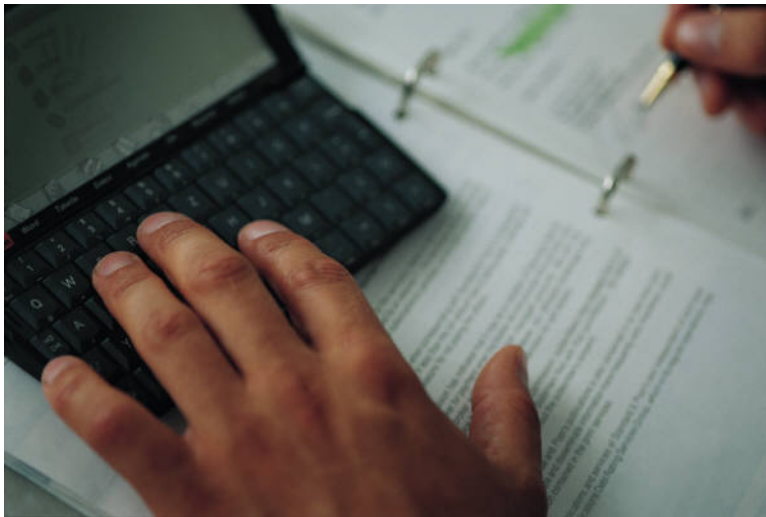

- Conduct Program Office sponsored SCAMPI As?
 - Requires core team to re-appraise contractors
- Verify completion of all process improvement activities outlined in approved Process Improvement Plan



Way Ahead - 2

How do we “maintain” the process improvement/process maturity focus to ensure consistent levels of performance/execution?

- The Program Office is working to develop a multi-year plan for continual assessment/monitoring
 - Additional appraisal for all contractors (cost/benefit)
 - “Spot check” areas of known deficiency
 - Appraisals for projects with performance issues
 - Appraisals for projects that fall within another organizational unit than “representative” project



Way Ahead - 3

Beginning to analyze SCAMPI-B for Contract Monitoring results against product quality to determine if there are correlations

- Could impact risk management/corrective actions in the future



Summary



Summary - 1

SCAMPI-Bs for Contract Monitoring were very positive for Mission Planning

- Provided insight into contractor processes and potential program risks

Consistency is key

Appraisal results have become a useful source of data to assist in program management activities

- PMs can focus attention on areas of the project that have highest risk due to inconsistent (or non-existent) standard processes



Summary - 2

SCAMPI-Bs for Contract Monitoring started as a way to do a “quick check” of contractor CMMI requirement compliance – and have now become a powerful management tool

Savvy consumers can utilize SCAMPI-Bs for Contract Monitoring as part of their management “tool box”



Contact Information

Lorraine Adams

Member of the Technical Staff

Software Engineering Institute

4500 5th Avenue

Pittsburgh, PA 15213

412-268-7777

ladams@sei.cmu.edu

Kathy Bastien

Senior Process Manager

BlueForce LLC

1919 Commerce Drive, Suite 400

Hampton, VA 23666

603-548-5936

kbastien@blueforcellc.com



Software Engineering Institute

Carnegie Mellon

SCAMPI-B for Contract Monitoring
Lorraine Adams and Kathy Bastien
March 2007

© 2006 Carnegie Mellon University



Software Engineering Institute

Carnegie Mellon
